



VICINITY MAP

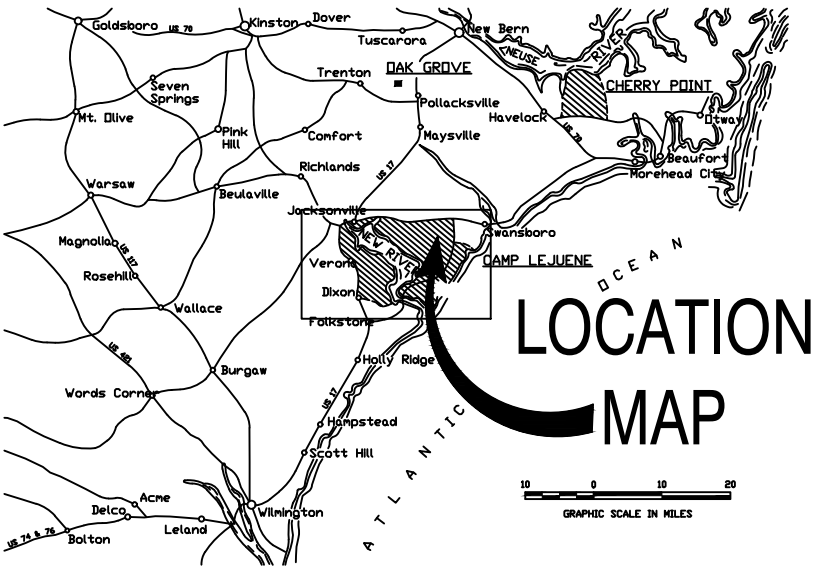


LOCATION MAP

LOCATION MAP

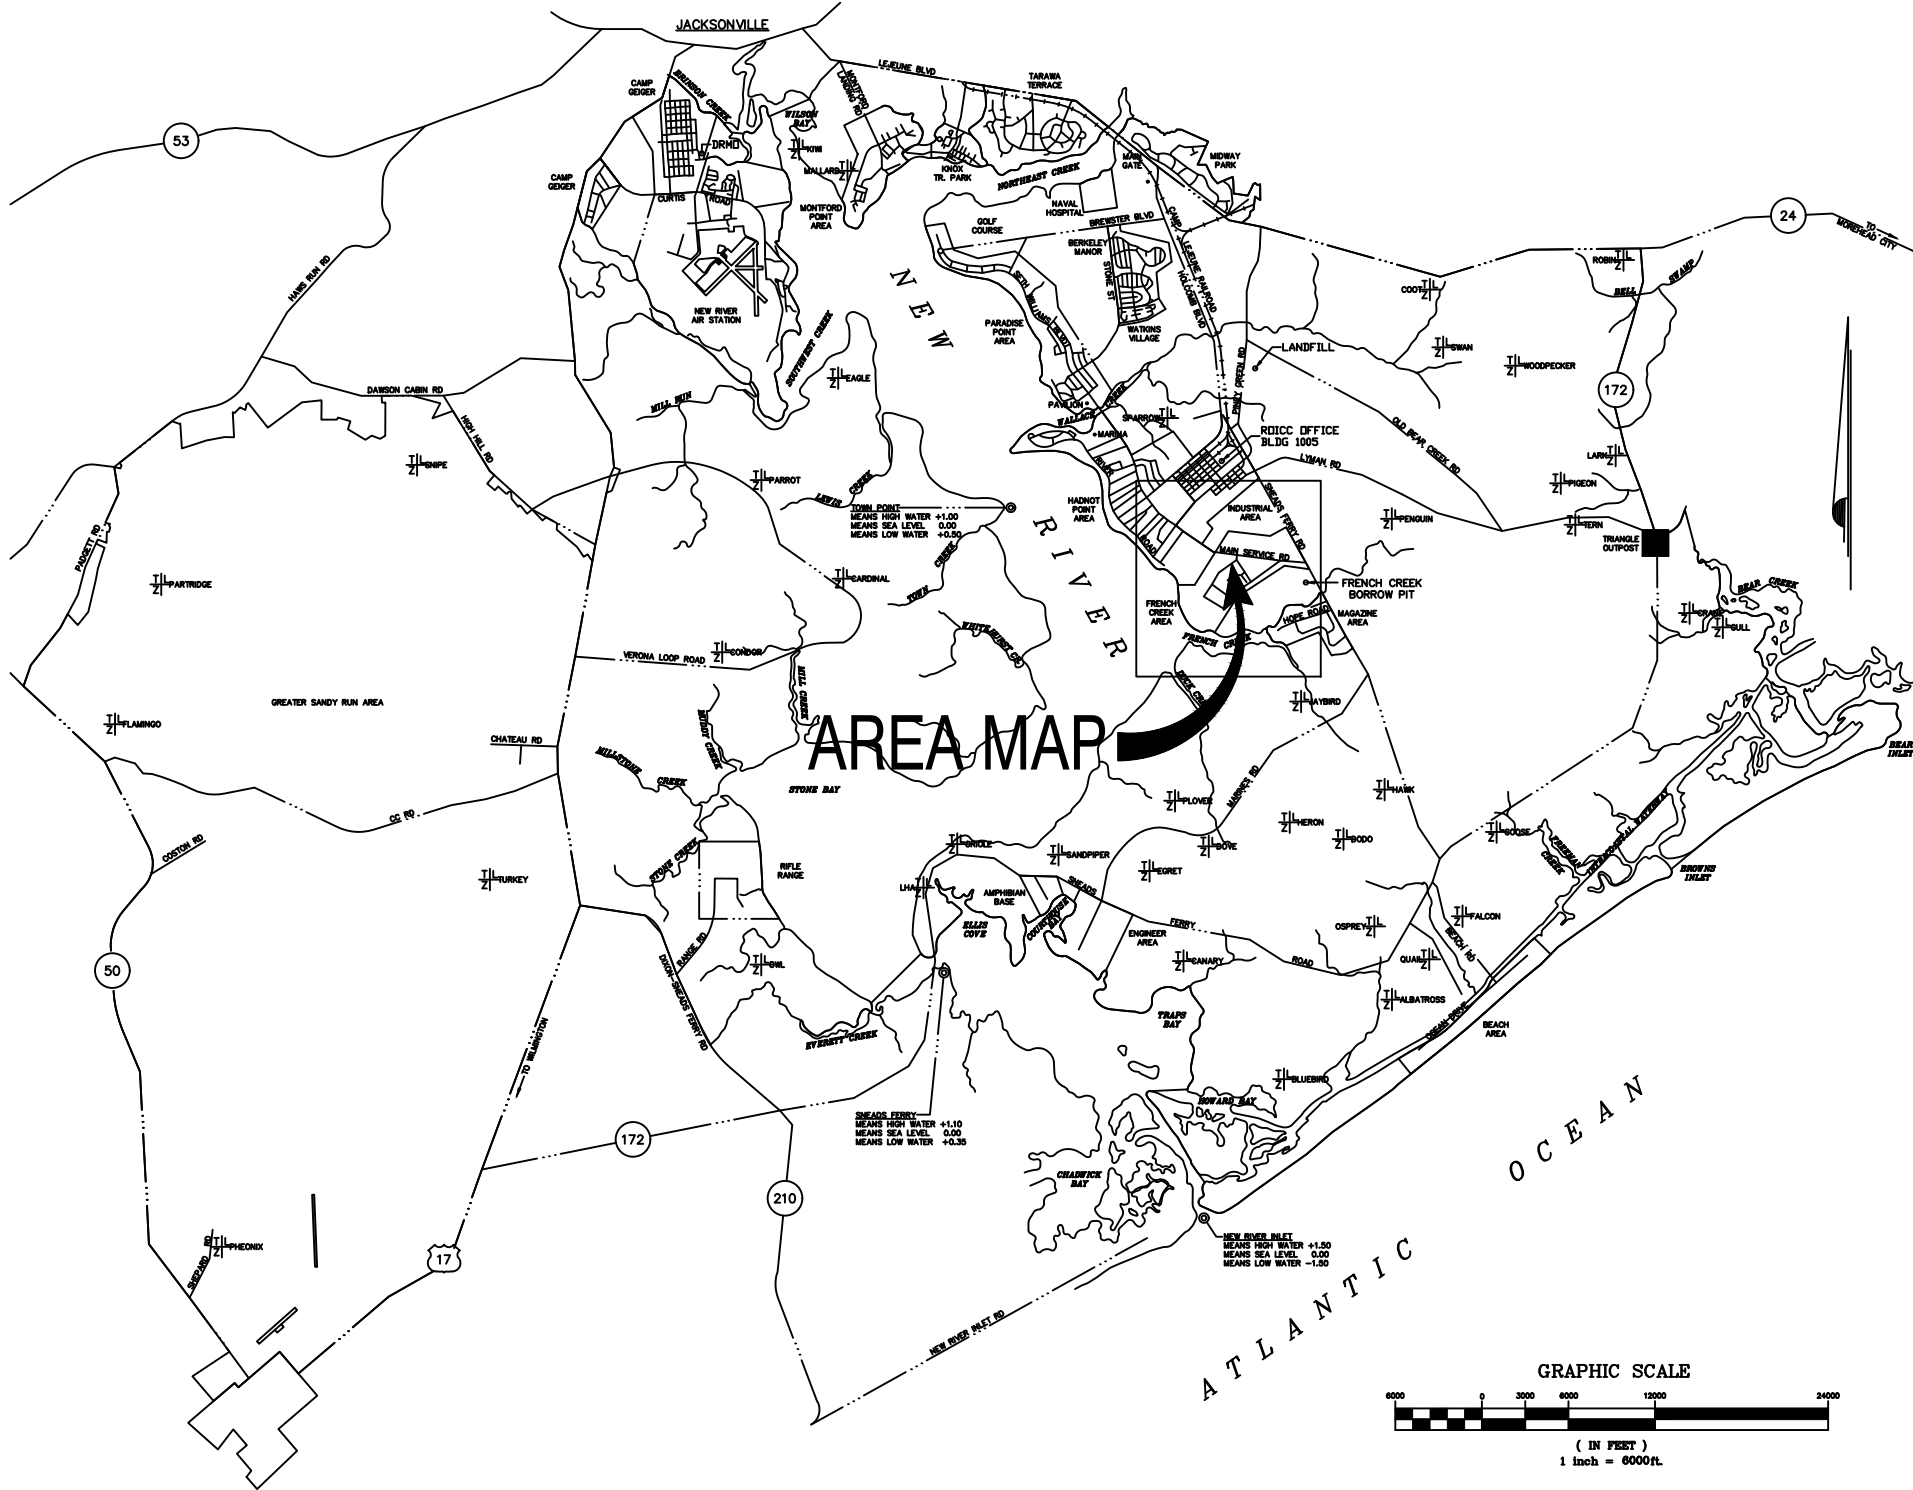

AREA MAP

AREA MAP

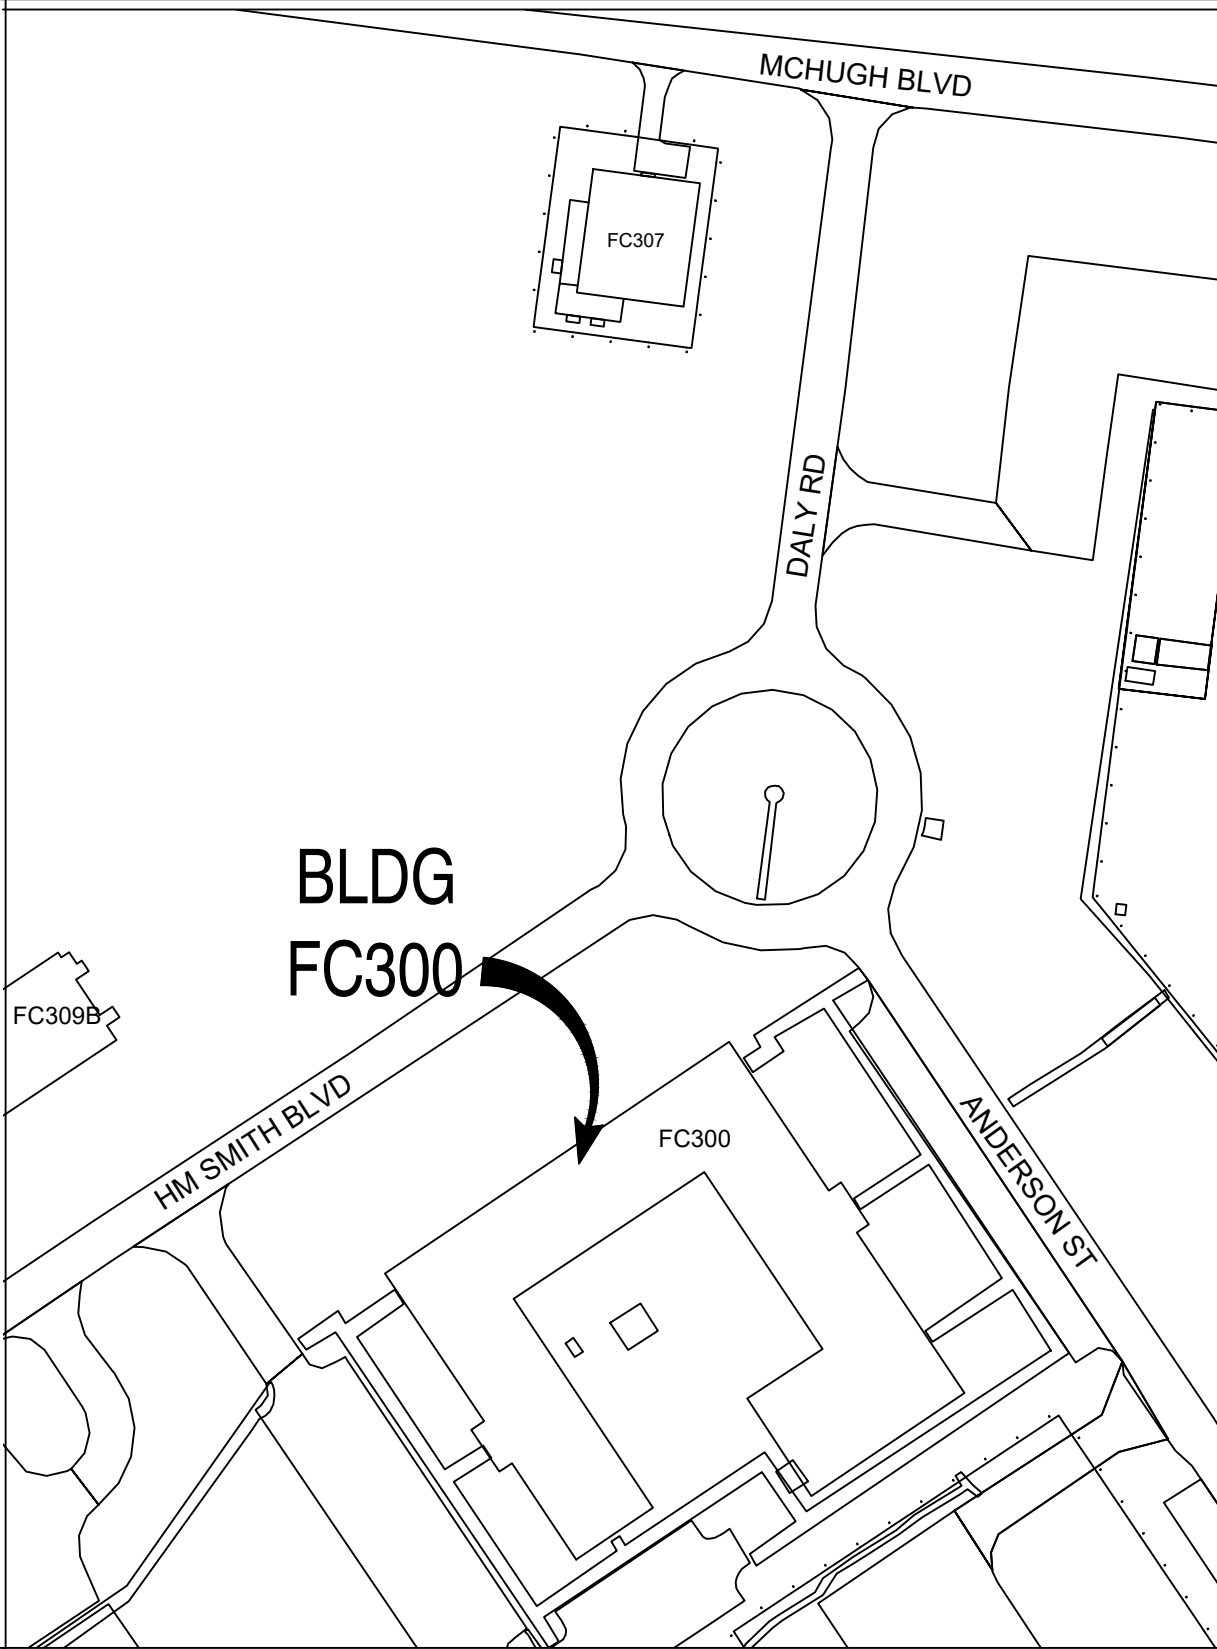

BLDG FC300

DRAWING INDEX

SHEET #	SHEET NAME
T-1	TITLE SHEET, AREA MAPS
A1	NOTES/OVERALL PLAN
A2	ARCHITECTURAL PLANS
M1	MECHANICAL PLANS
E1	ELECTRICAL PLANS

BLDG FC300 SHEET 1 OF 5
MAXIMO # 5462330
DWG. MARK RANSIELL PROJECT # 25-0447

FC300 SERVER ROOM
MODERNIZATION
USMC CAMP LEJEUNE

T1

TITLE PAGE

1005 OFFICE REPAIRS

SCOPE OF WORK: The contractor shall provide all material, labor, equipment and supervision required to accomplish the following.

GENERAL DESCRIPTION: This scope of work is to be accomplished at Building FC300 located on H.M. Smith Blvd. aboard, Camp Lejeune, North Carolina. The work includes demo existing suspended acoustical ceiling tile, lights and mechanical items in existing server room. Contractor shall install new A.C.T. ceiling, electrical and mechanical items as per drawings.

DETAILED REQUIREMENTS AND SPECIFICATIONS: The contractor shall take his own field measurements in determining required materials and costs for the following.


SPECIAL SCHEDULING AND ACCESS: Access and scheduling to the work area shall be arranged through Contracting Officer's Representative for the OICC office and the tenant of the building. Point of Contact for access to building is SSgt Werline (910-450-5221).

NOTES:

1. The measurements and quantities furnished here are for reference only. The contractor is responsible for actual field verification prior to bidding, ordering material and during every step of construction for existing surfaces, dimensions and conditions.
2. Repair, refinish of areas damaged or disturbed by new work to be provided under this contract.
3. Contractor may ONLY use the Camp Lejeune Sanitary landfill for the disposal of asbestos containing materials, building products with tightly adhered lead containing paint, non-contaminated clean dirt and clean gravel. the hours of operations are 0730-1530 Monday- Thursday and 0730-1430 on Friday. delivery of acceptable materials (identified above) shall be by appointment only. Appointment made by phone at 1-910-457-5011 or 1-910-451-2946.
4. All other contractor generated material shall be weighed through the Base Landfill scales before being removed from the Base. Contractor utilizing the base scale will require Contracting Officers assisted per-registration with the Landfill manager.
5. The Contracting officer will register the contract via E-mail, with the base landfill. All haul vehicles will maintain a secure vehicle placed as a condition to utilize the scale. E-mail the contractors information to the Landfill Clerk, include the name on the Prime contractor, contract number, job name / description, completion date and whether or not any above material will be delivered to the Landfill.
6. Prior to performing "HOT WORK" (welding, cutting, ect.) or operating other flame -producing spark producing devices, a written permit shall be requested from the Fire Division. CONTRACTORS ARE REQUIRED TO MEET ALL CRITERIA BEFORE A PERMIT IS ISSUED. The contractor will provide at least two (2) twenty (20) pound 4A:20 BC rated extinguishers for normal "HOT WORK". All extinguishers shall be current inspection tagged, approved safety pin and tamper resistant seal. It is also mandatory to have a designated FIRE WATCH for any "HOT WORK" done at this activity. The Fire watch shall be trained in accordance with NFPA 51B and remain on site for a minimum of thirty (30) minutes after work is completed.
7. Contractor is to be aware of all rules, regulation and codes required for successful completion of project.

SUBMITTALS:

1. AFTER AWARD: The Contractor shall furnish the DSC-EMI, material, specifications for selection and approval prior to the ordering and installation of said materials.
2. The contractor is required to submit a schedule detailing when they and or any subcontractor will be working. The schedule must be approved by Government before beginning work.
3. The contractor shall submit the manufacture's product specifications, complete with technical products data for all of the material being used in this process. The product specification shall as a minimum, provide the technical details on the following items.
4. Submit:
 - A. SHOP DRAWINGS.
 - B. INSTALLATION DRAWINGS /shop drawings
 - C. PRODUCT DATA
 - C.A. Manufactures technical data Sheet
 - C.B. Material Safety Data Sheets (MADA)
 - C.C. Maintenance Data
 - D. WARRANTY (10 year Commercial Limited Warranty)
6. Qualifications:
 - 6.1. Fabricator Qualifications: Minimum of three years documented experience in construction similar in scope and complexity to this Project. Currently certified by the manufacturer as acceptable fabricator.
 - 6.2. Installer Qualification: Minimum of three years documented installation experience for project similar in scope and complexity to this project and currently certified by manufacturer as an acceptable installer.

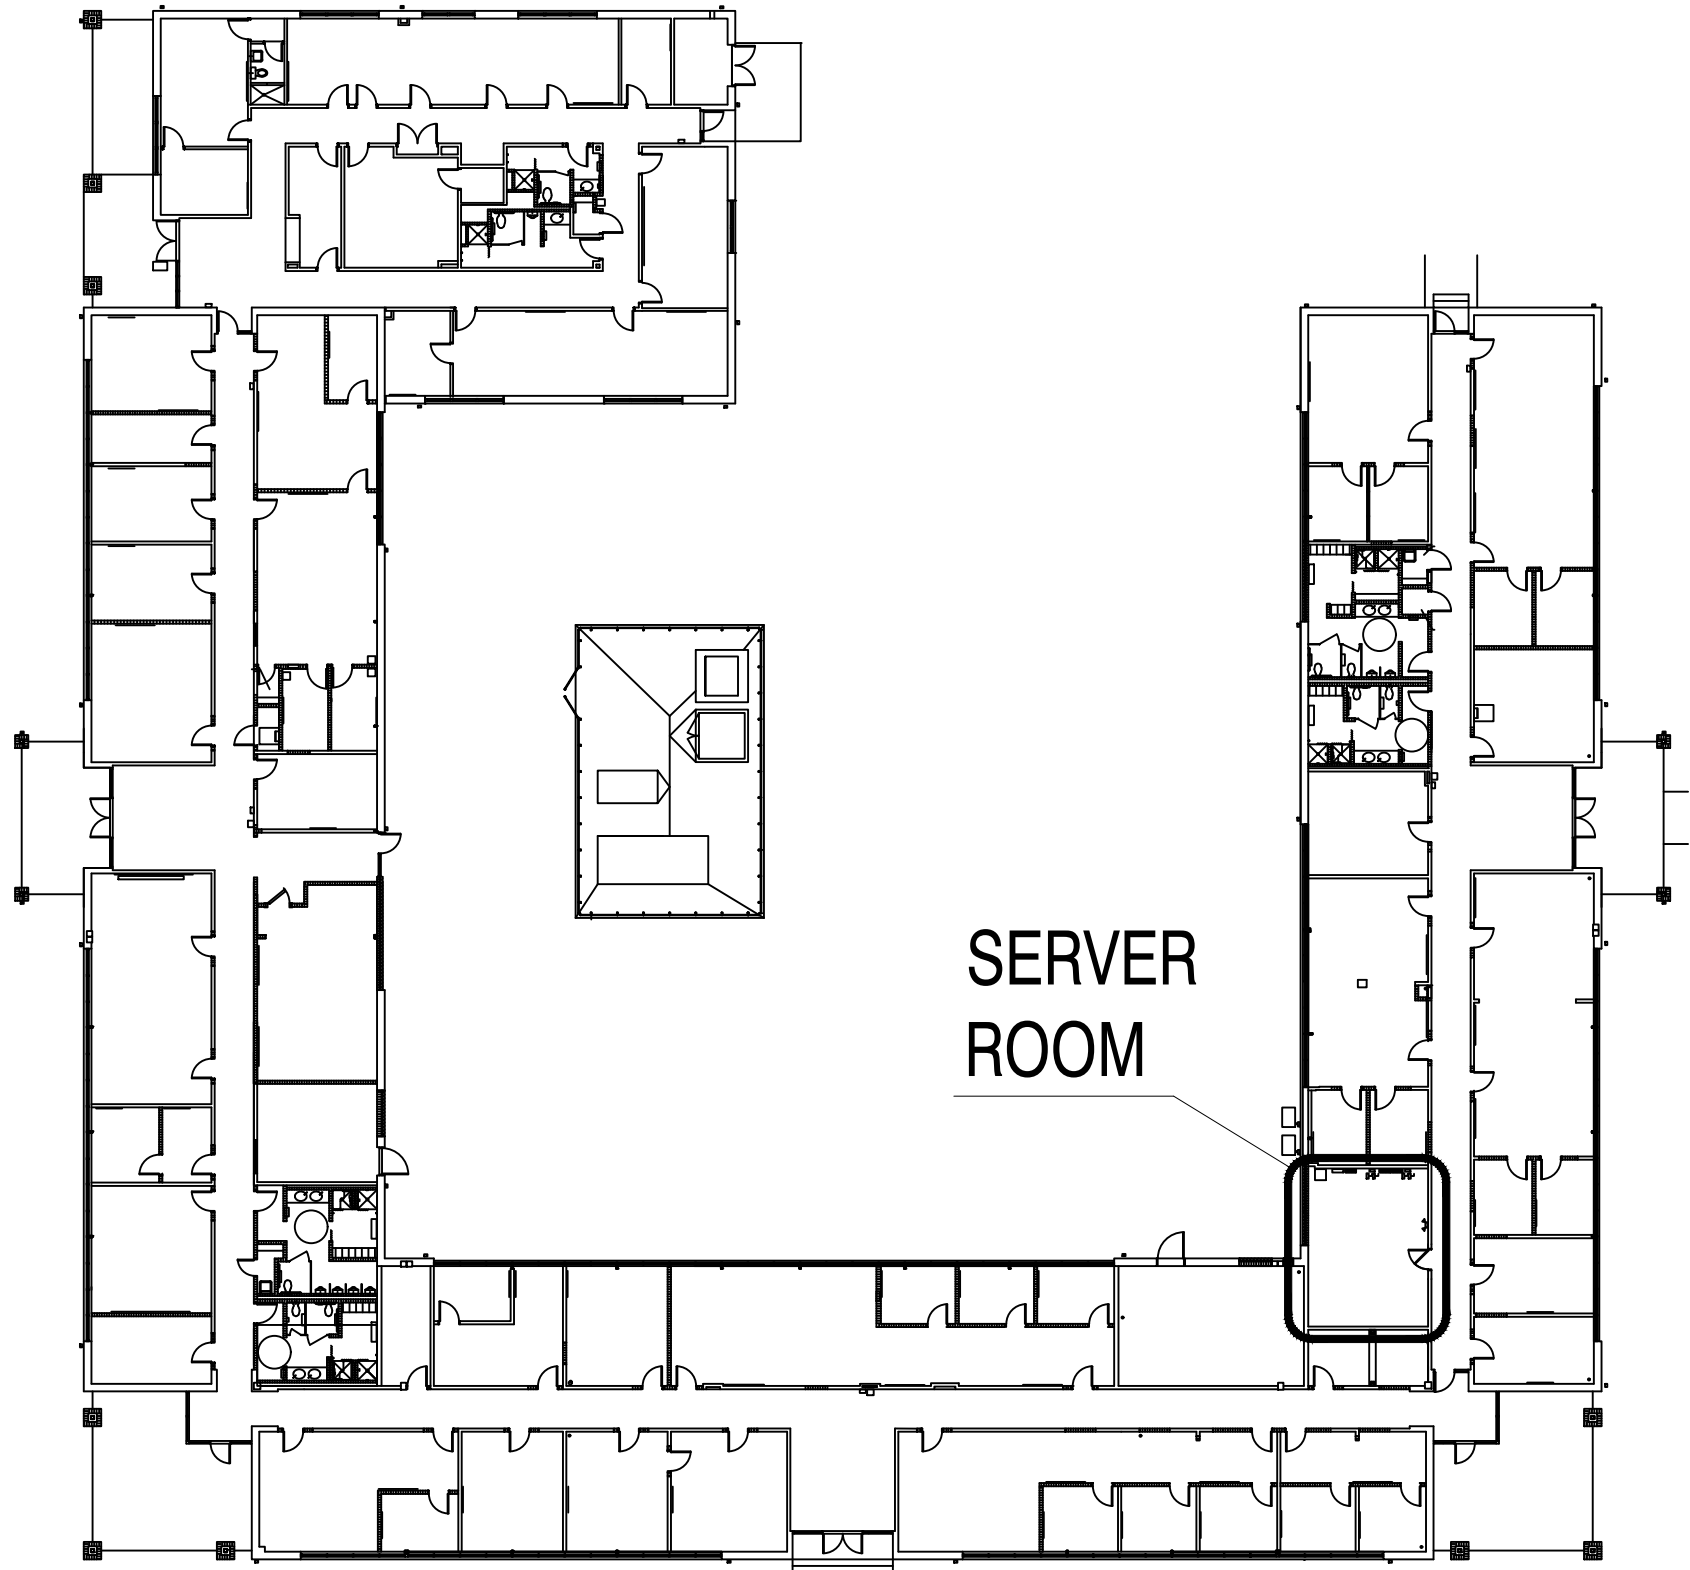

1
A1


FC300 OVERALL PLAN

NOT TO SCALE

NOTES, OVERALL PLAN

BLDG FC300	SHEET 2 OF 5
FC300 SERVER ROOM MODERNIZATION	MAXIMO # 5462330
USMC CAMP LEBJUNE	DWG. MARK RANSSELL PROJECT # 25-0447
A1	

RENOVATION NOTES	
1	NEW SOLID CORE 90 MINUTE RATED WOOD DOOR W/ X-10 GSA APPROVED COMBINATION LOCK MEETING FEDERAL SPEC. FF-L-2740 PER MCD5530.14A. NEW 90 MINUTE RATED METAL DOOR FRAME.
2	NEW A.C.T. CEILING TILES, GRID AND SUPPORTS. A.C.T. TILES TO MATCH EXISTING STYLE AND SIZE.
3	EXISTING FIRE SUPPRESSION SPRINKLER HEADS TO REMAIN. REPAIR ANY HEADS DAMAGED DURING CONSTRUCTION.
4	PATCH PLYWOOD AT ALL AREAS OF MECHANICAL AND ELECTRICAL REMOVAL AND SAND SMOOTH. PAINT PLYWOOD AND TRIM TO MATCH EXISTING. CLEAN WALL BELOW PLYWOOD TO REMOVE ALL STAINING.

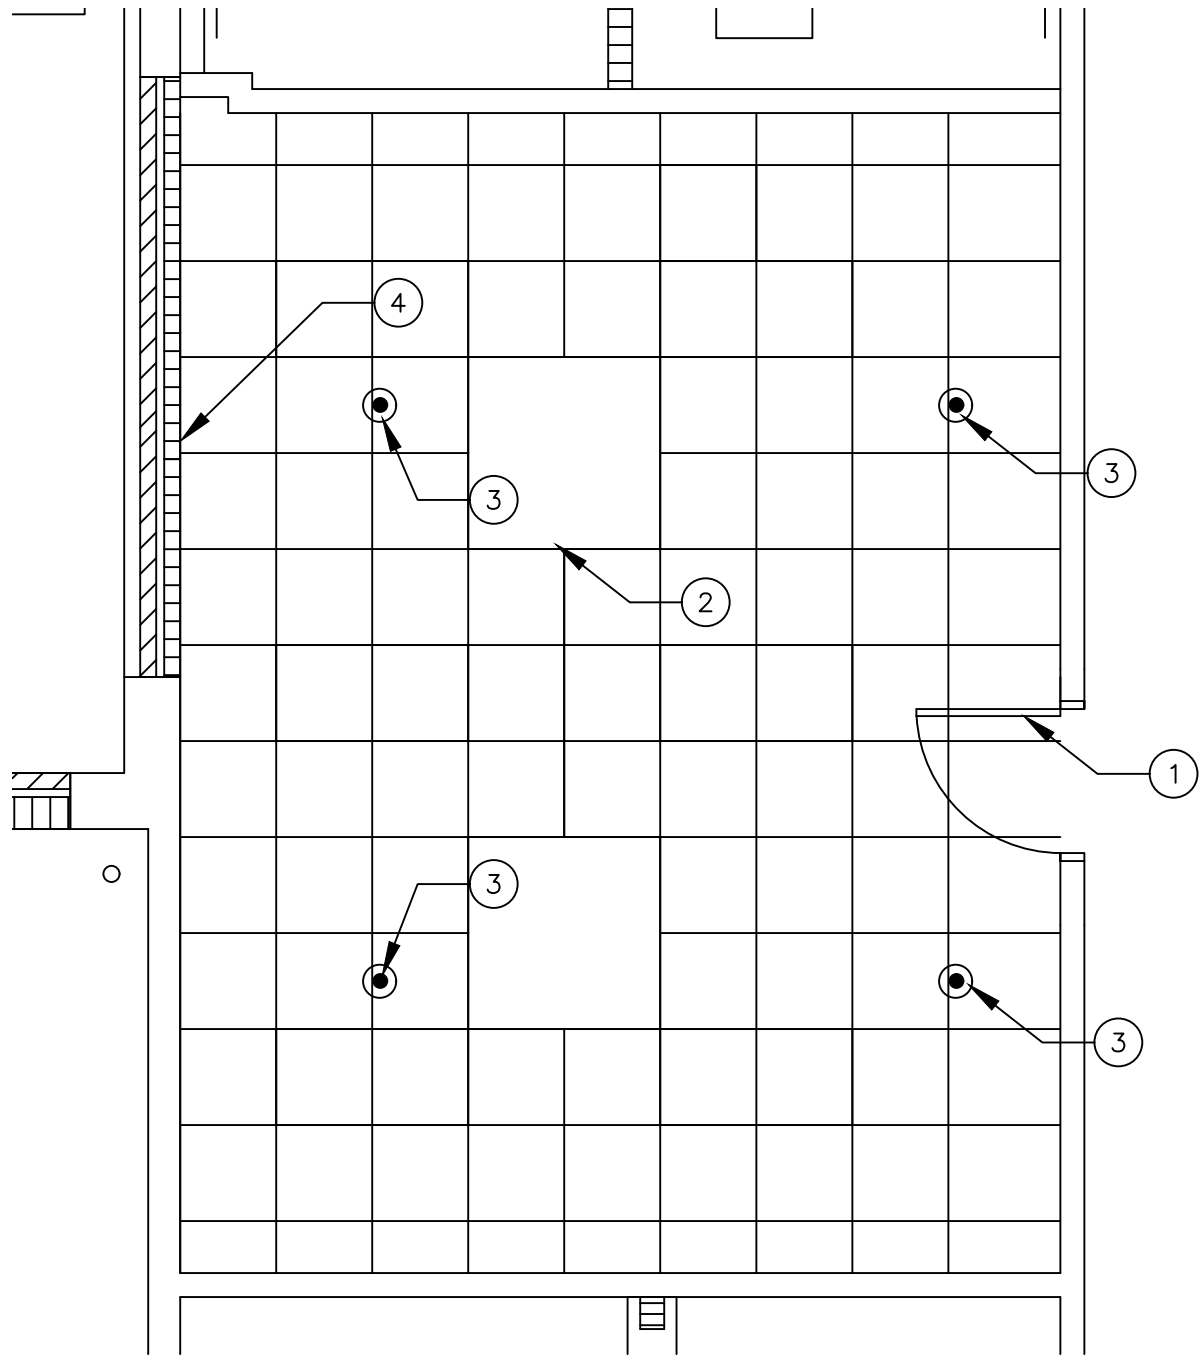

2

A2

SERVER ROOM RENO PLAN


1/4" = 1'-0"

0

5'

10'

DEMOLITION NOTES	
1	REMOVE EXISTING DOOR & FRAME. PREPARE FRAME FOR RECEIPT OF NEW DOOR.
2	REMOVE EXISTING A.C.T. CEILING TILES, GRID AND SUPPORTS. PREPARE FOR NEW A.C.T. CEILING TILES.
3	EXISTING FIRE SUPPRESSION SPRINKLER HEADS TO REMAIN. PROTECT.
4	EXISTING PLYWOOD AND WOOD TRIM OVER EXISTING GLASS BLOCK. PREPARE FOR NEW PAINT.
5	EXISTING ELECTRICAL FIXTURE. SEE ELEC DRAWINGS
6	EXISTING MECHANICAL ITEM IN CEILING. SEE MECHANICAL DRAWINGS.

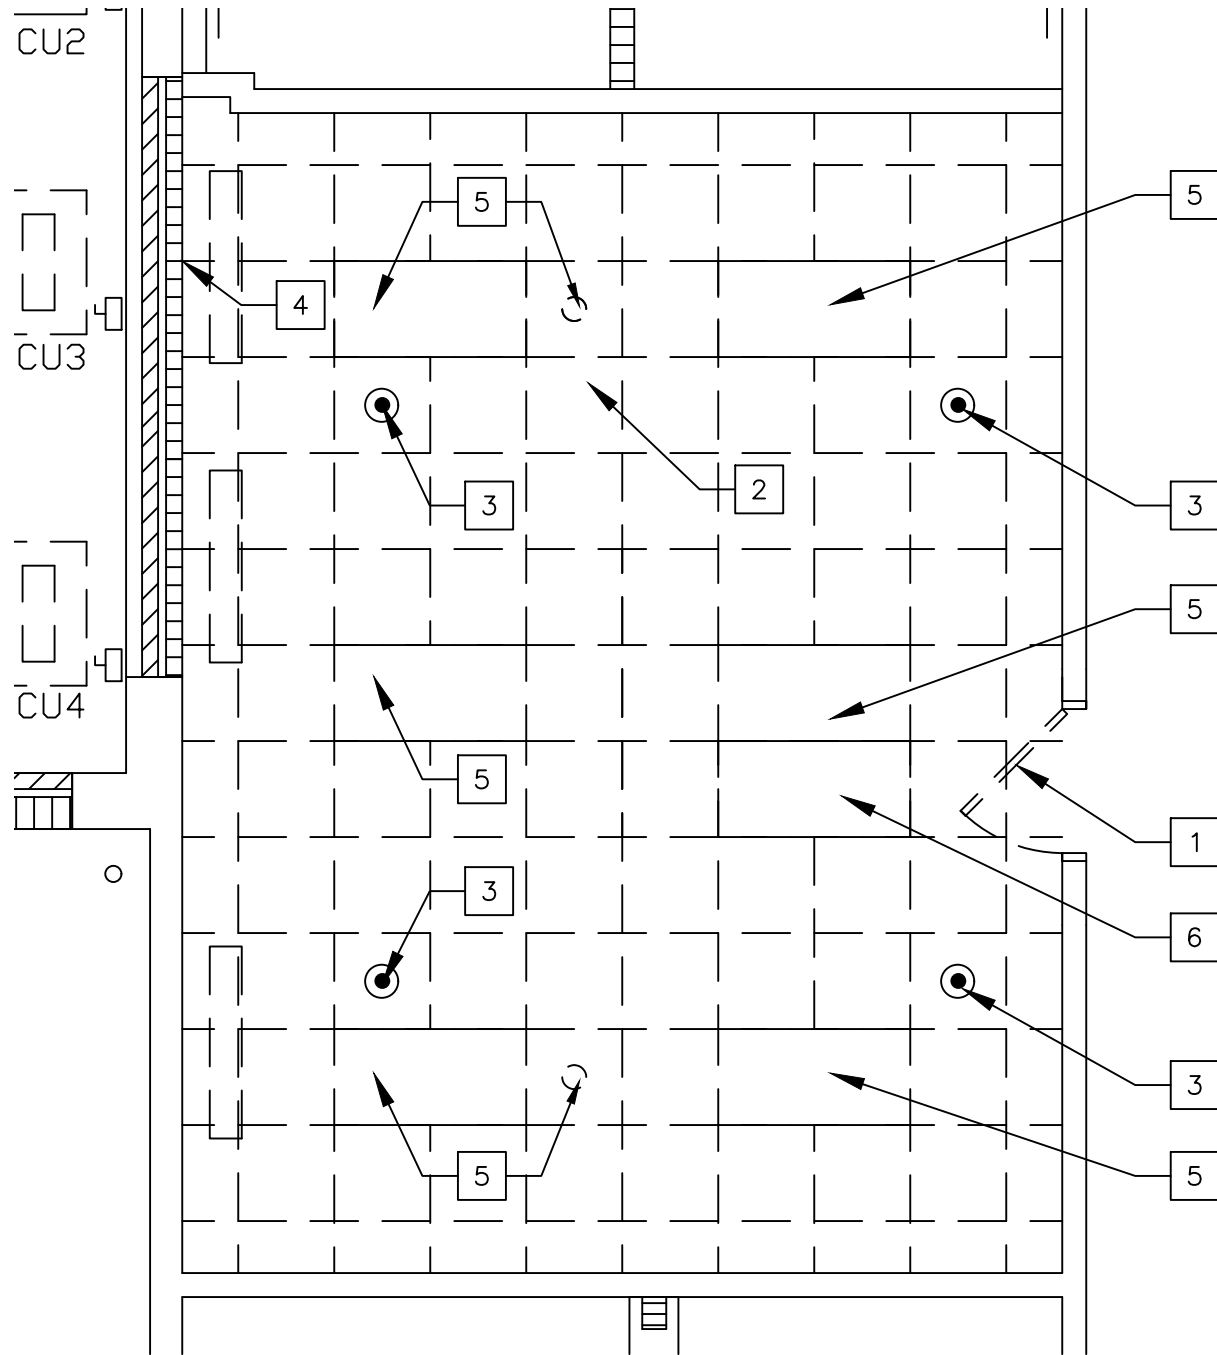

1

A2

SERVER ROOM DEMO PLAN


1/4" = 1'-0"

0

5'

10'

MECHANICAL RENOVATION NOTES




- 1

PROVIDE 2 NEW 48,000 BTU CEILING CASSETTES AND 2 NEW HEAT PUMP CONDENSERS. REUSE THE EXISTING CONCRETE PADS FOR CU 3&4. UTILIZE THE EXISTING PENETRATIONS FOR THE REFRIGERANT PIPING, CONDENSATE DRAINS AND THE ELECTRICAL AND CONTROL WIRING. PROVIDE UV PROTECTANT FOR THE REFRIGERANT LINE INSULATION THAT MEETS THE MFR'S RECOMMENDATIONS. PROVIDE NEW EQUIPMENT DISCONNECTS THAT MEET THE REQUIREMENTS FOR THE NEW EQUIPMENT.
- 2

INSTALL 2 NEW CEILING CASSETTES THAT MEET OR EXCEED THE OPERATING CHARACTERISTICS OF DAIKIN RZR48TAVJU-FCQ48TAVJU- BYCP125K-W. THE UNITS NEED WIRED , WALL-MOUNT CONTROLLERS. THE UNITS WILL NEED TO BE EQUALLY SPACED FOR MAXIMUM COVERAGE. IF THE CEILING CASSETTES REQUIRE THEIR OWN POWER SOURCE, UTILIZE PANEL UPS 120/208.
- 3

PROVIDE 1-24"X24" WITH 8"ROUND NECK, GRID MOUNTED ALUMINUM RETURN DIFFUSER (IN THE COMM ROOM)TO ACT AS A TRANSFER FROM THE ADJACENT OFFICE. PROVIDE 1- 24"X24" WITH 8" ROUND NECK, GRID MOUNTED ALUMINUM, RETURN DIFFUSER (IN THE ADJACENT OFFICE) TO ACT AS A TRANSFER. INSULATED 8" FLEXIBLE DUCT CAN BE USED AS THE TRANSFER DUCT.

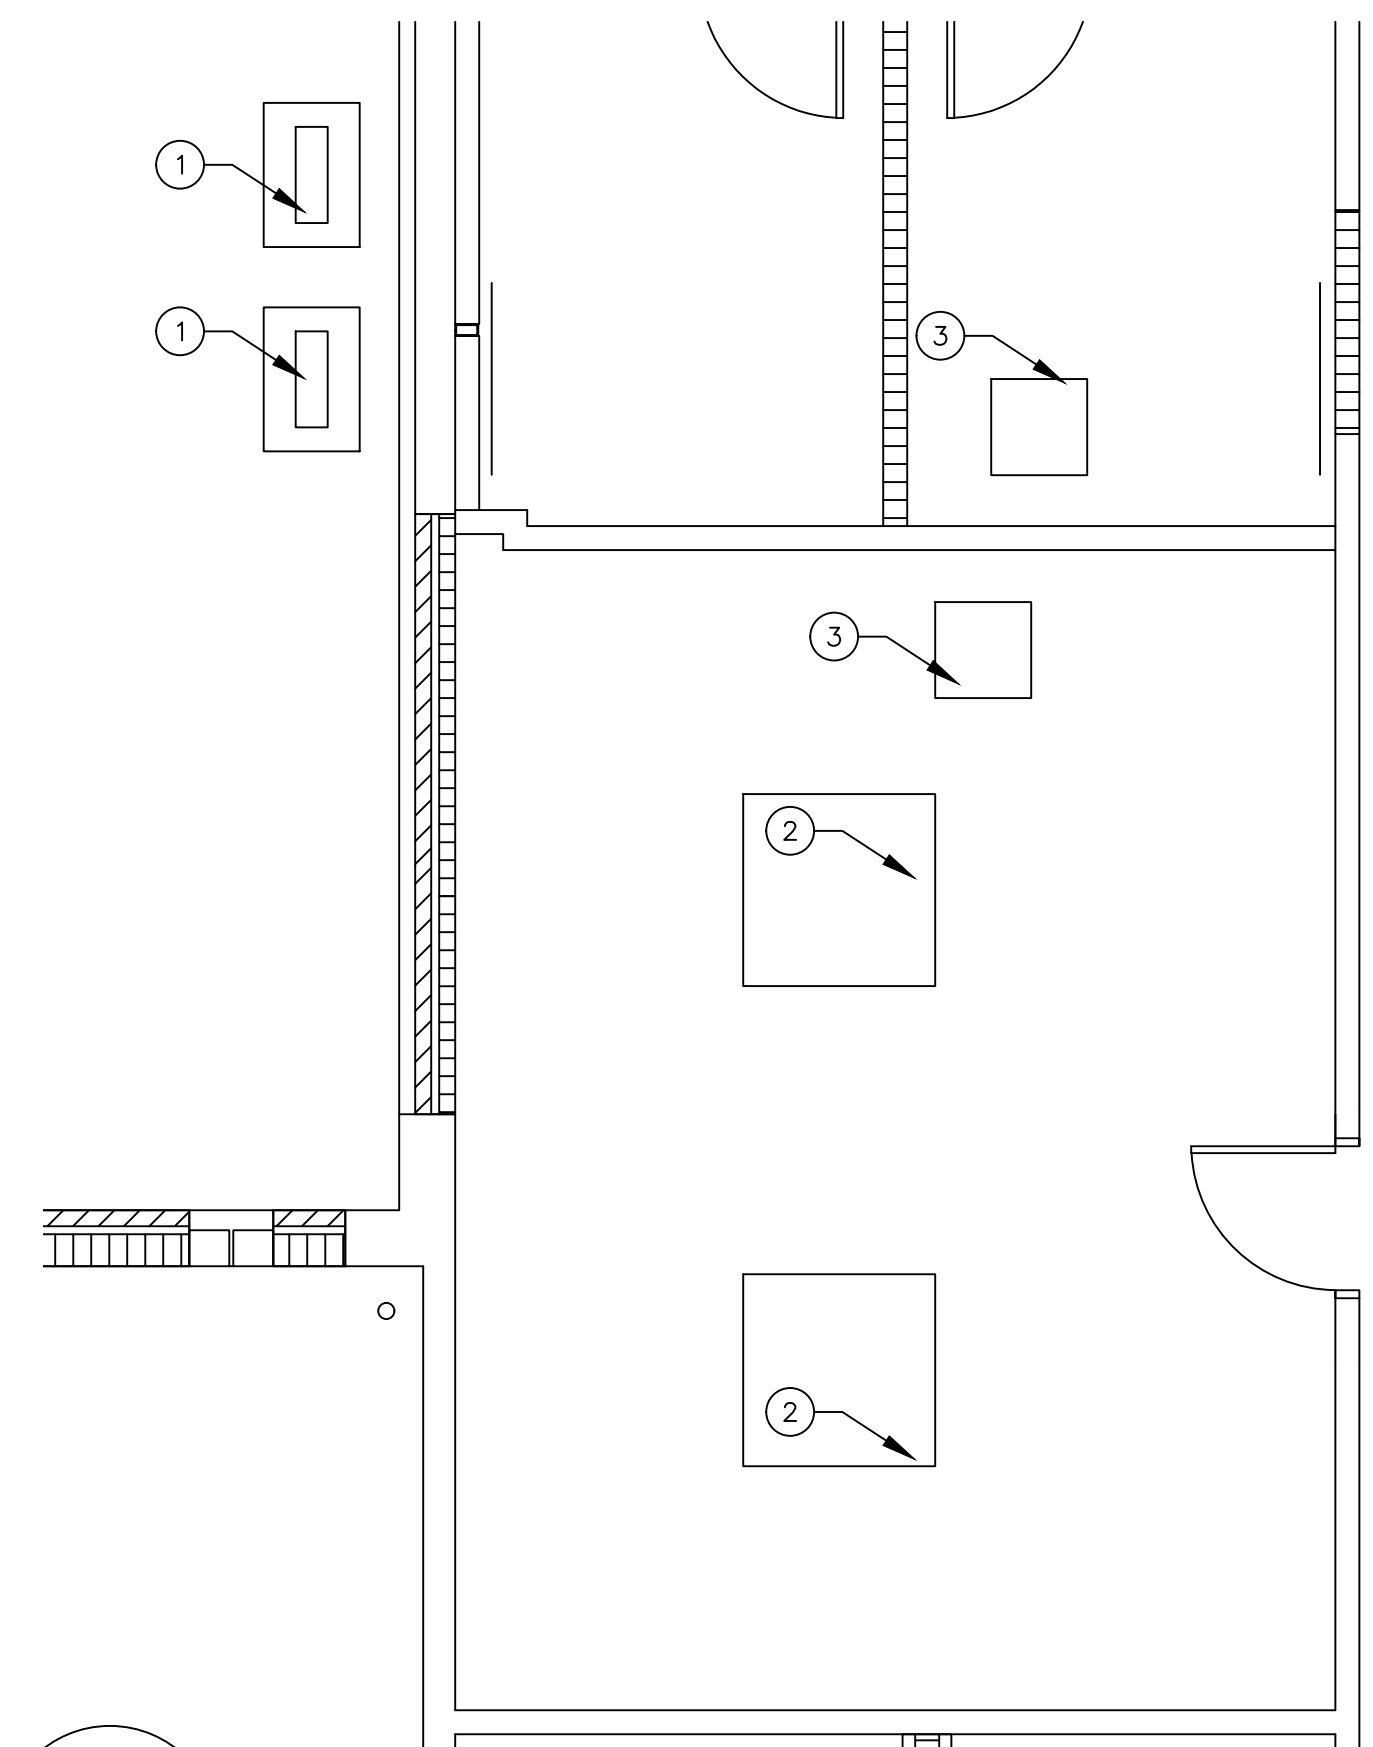

2

M1

SERVER ROOM MECHANICAL RENO PLAN

1/4" = 1'-0"

0 5' 10'


MECHANICAL DEMOLITION NOTES



- 1

SECURE POWER TO EXISTING CONDENSER 1-4. DEMO ELECTRICAL WIRING FROM MDP# TO EXTERIOR EQUIP., TO INCLUDE EXISTING EQIDP. DISCONNECTS. RECOVER REFRIGERANT FROM CU 1-4. DEMO EXTERIOR CU'S AND PIPING INCLUDING PIPE HANGERS. DEMO CONCRETE PAD FOR CU 1& 2, GRADE AREA WHERE PADS ARE REMOVED TO ASSURE AREA IS LEVEL.
- 2

DEMO INTERIOR AHU'S AND CEILING CASSETTE. DEMO ALL ASSOCIATED WIRING AND PIPING (REFRIGERANT AND DRAIN PIPING). REMOVE ALL WIRING BACK TO SOURCE. DEMO EXISTING UNIT SUPPORTS

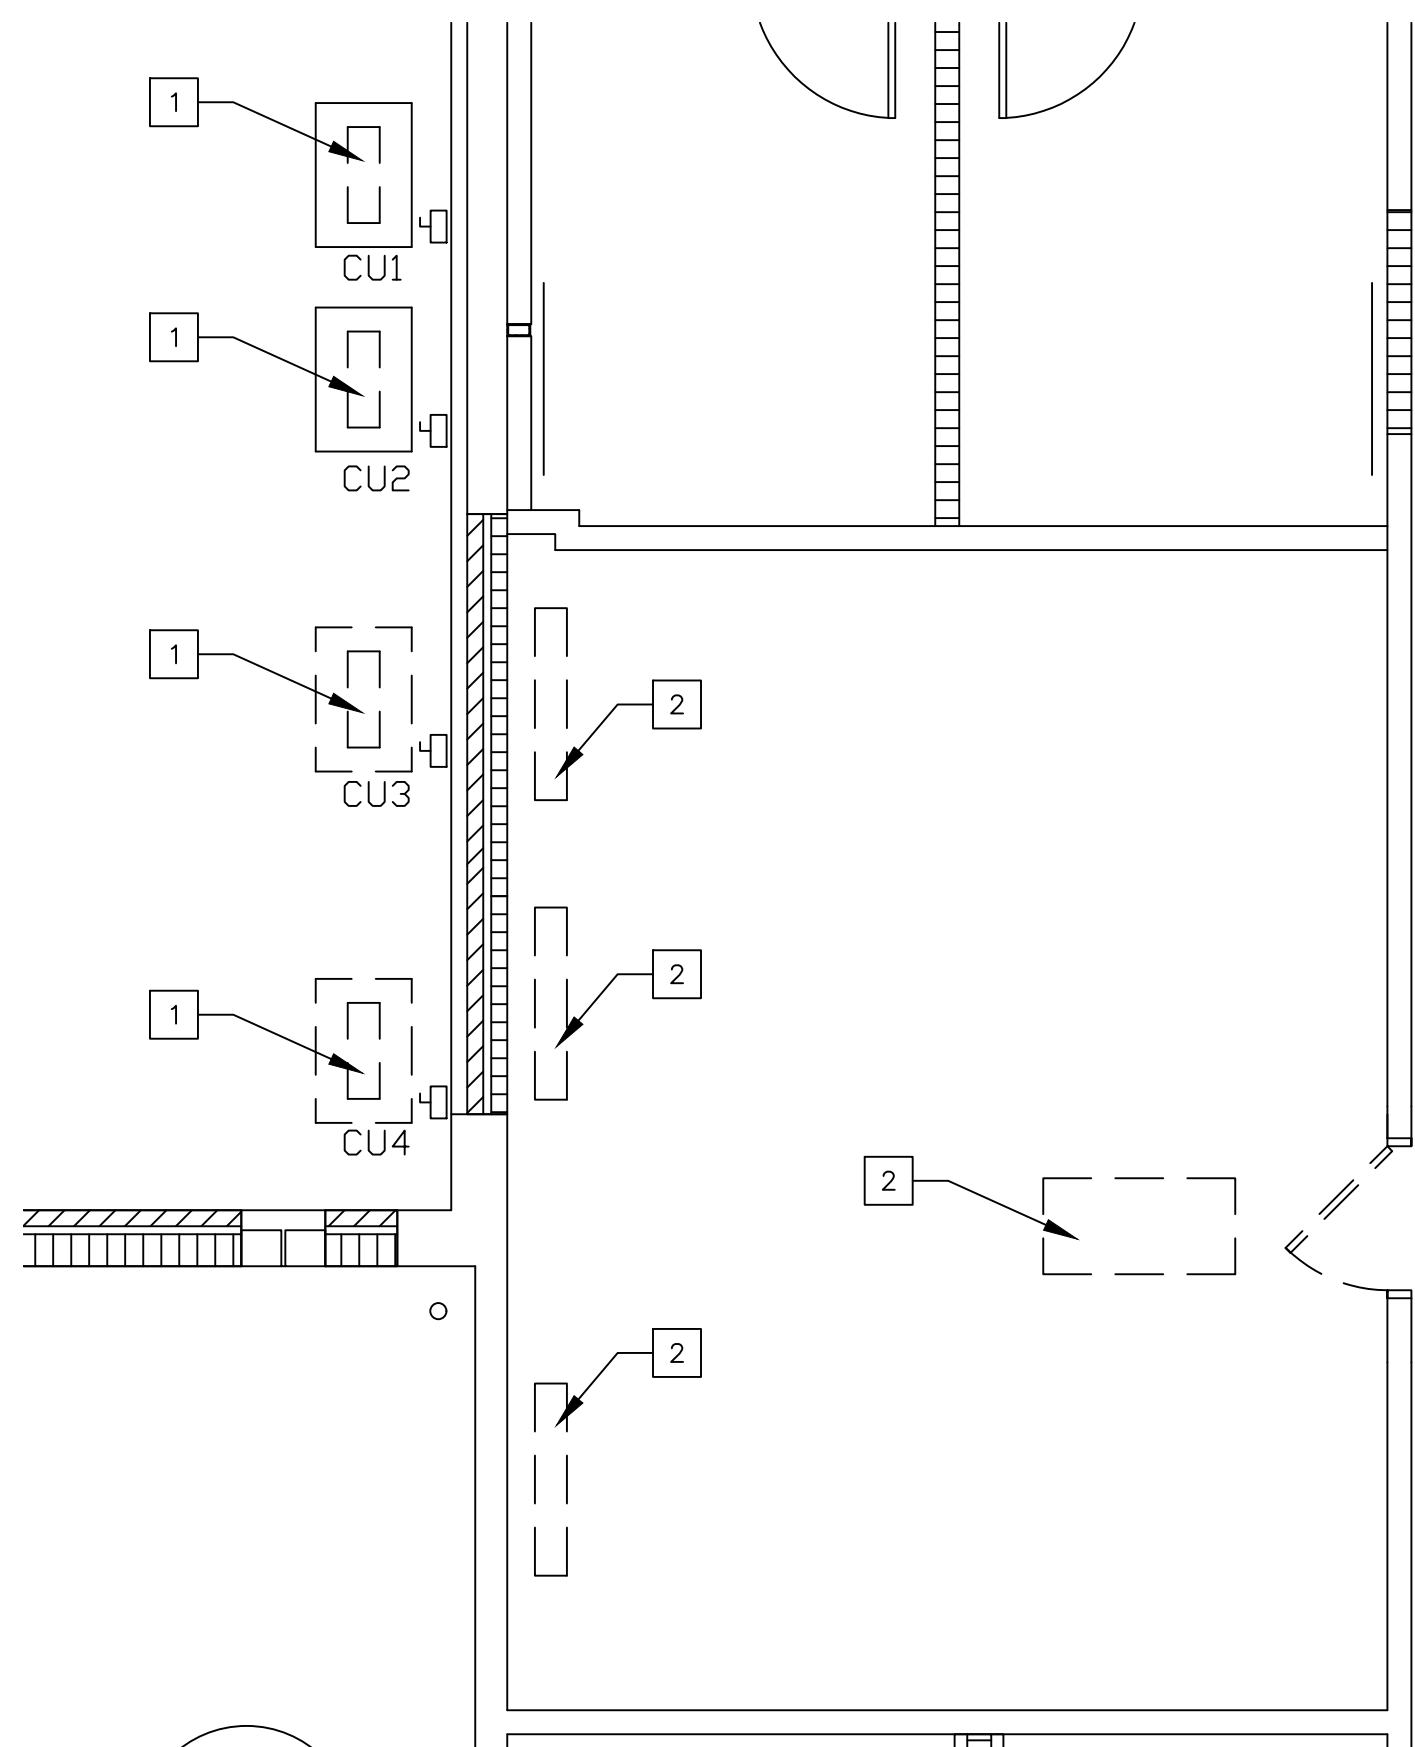

1

M1


SERVER ROOM MECHANICAL DEMO PLAN


1/4" = 1'-0"

0 5' 10'

ELECTRICAL RENOVATION NOTES

1	INSTALL 9EA NEW CEILING MOUNTED 3300 LUMEN, 3500K COLOR TEMPERATURE, 2FT X 2FT LED TROFFERS AS INDICATED. THE BASIS OF DESIGN IS LITHONIA MODEL 2VTL2 33L ADPT LP835. THE LIGHT FIXTURES SHALL PRODUCE A MINIMUM ILLUMINANCE LEVEL OF 50 FOOTCANDLES AT 3FT ABOVE FINISHED FLOOR. THE LIGHTS SHALL BE CONTROLLED WITH 1EA WALL MOUNTED SINGLE POLE SWITCH AT THE DOOR.
2	INSTALL 2EA 30A 240V NEMA 3R HEAVY DUTY NON-FUSED DISCONNECT AT HEAT PUMP LOCATION 3 AND 4. REPLACE EXISTING GFCI RECEPTACLE AND INSTALL NEW IN-USE COVER.
3	INSTALL NEW CIRCUIT BREAKERS AND FEEDER CONDUCTORS FOR NEW HVAC EQUIPMENT AT PANEL MDP. CIRCUIT BREAKER AND CONDUCTOR SIZES SHALL BE BASED ON MANUFACTURERS RECOMMENDATION.
4	REMOVE THE EXISTING PANEL LABELS AND RE-LABEL AS INDICATED
5	REMOVE THE EXISTING 16EA QUAD OUTLETS INSTALLED AT THE EDGE OF THE DROP CEILING. RELOCATE THE QUAD OUTLETS TO THE HEIGHT OF THE EXISTING FLUSH MOUNTED OUTLETS IN THE ROOM. RE-LABEL WITH NEW PANEL DESIGNATIONS.
6	2- 4 -TON Ceiling Cassettes Electrical- 208/230V 1 Phase 29.1 Amps Size - Outdoor Unit 52 15/16" H x 35 7/16" W x 12 5/8" D Indoor Unit 33 1/16" W x 33 1/16" D x 11 5/16H

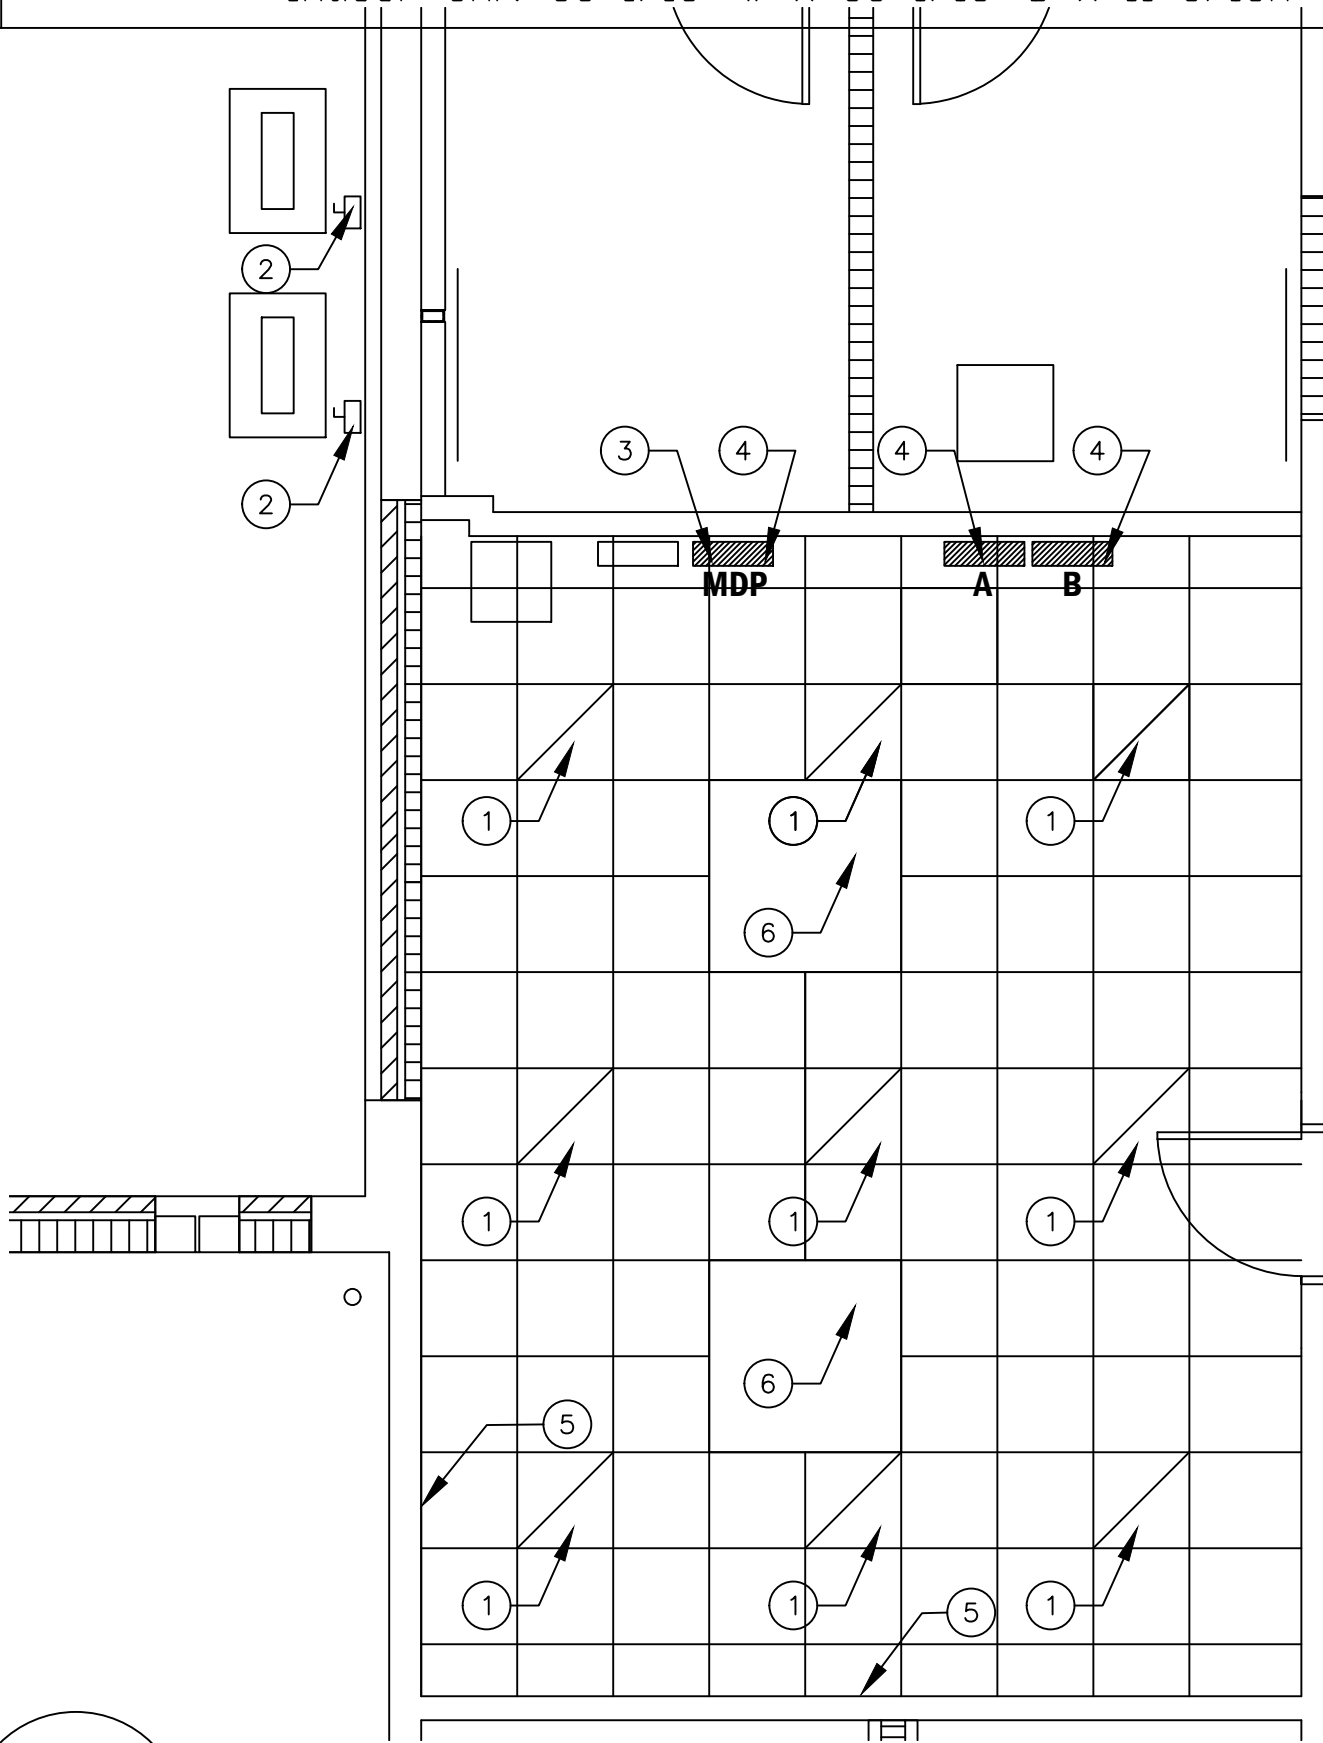


 = NEW LIGHT. SEE RENO NOTE #1

SERVER ROOM ELECTRICAL RENO PLAN

1/4" = 1'-0" 

ELECTRICAL DEMOLITION NOTES

1	REMOVE THE EXISTING INTRUSION DETECTION SYSTEM (IDS) COMPLETE. INCLUDING BUT NOT LIMITED TO DOOR DEVICES, CONTROL PANELS, CONDUIT AND CONDUCTORS.
2	REMOVE THE EXISTING UNINTERRUPTIBLE POWER SUPPLY (UPS) CONTROLS COMPLETE. INCLUDING BUT NOT LIMITED TO DISCONNECT/BYPASS SWITCHES, SAFETY SWITCHES, SECONDARY CONDUIT AND CONDUCTORS. RE-ROUTE THE EXISTING FEEDER CONDUIT AND CONDUCTORS TO THE SUB-PANELS.
3	REMOVE THE EXISTING CEILING MOUNTED LIGHT FIXTURES AND SMOKE DETECTORS COMPLETE. INCLUDING BUT NOT LIMITED TO WALL SWITCHES, FIXTURE WHIPS, SMOKE DETECTOR MOUNTING BOXES, CONDUIT AND CONDUCTORS
4	REMOVE THE EXISTING WALL MOUNTED BATTERY-OPERATED EMERGENCY LIGHT AND TELEPHONE PLATE COMPLETE. TO INCLUDE CONDUIT AND CONDUCTORS BACK TO THE FIRST JUNCTION BOX ABOVE THE CEILING.
5	ABOVE THE EXISTING SUSPENDED CEILING, REMOVE ALL UNUSED/ABANDONED CONDUITS AND LABEL ANY UN-USED CABLES AS ABANDONED.

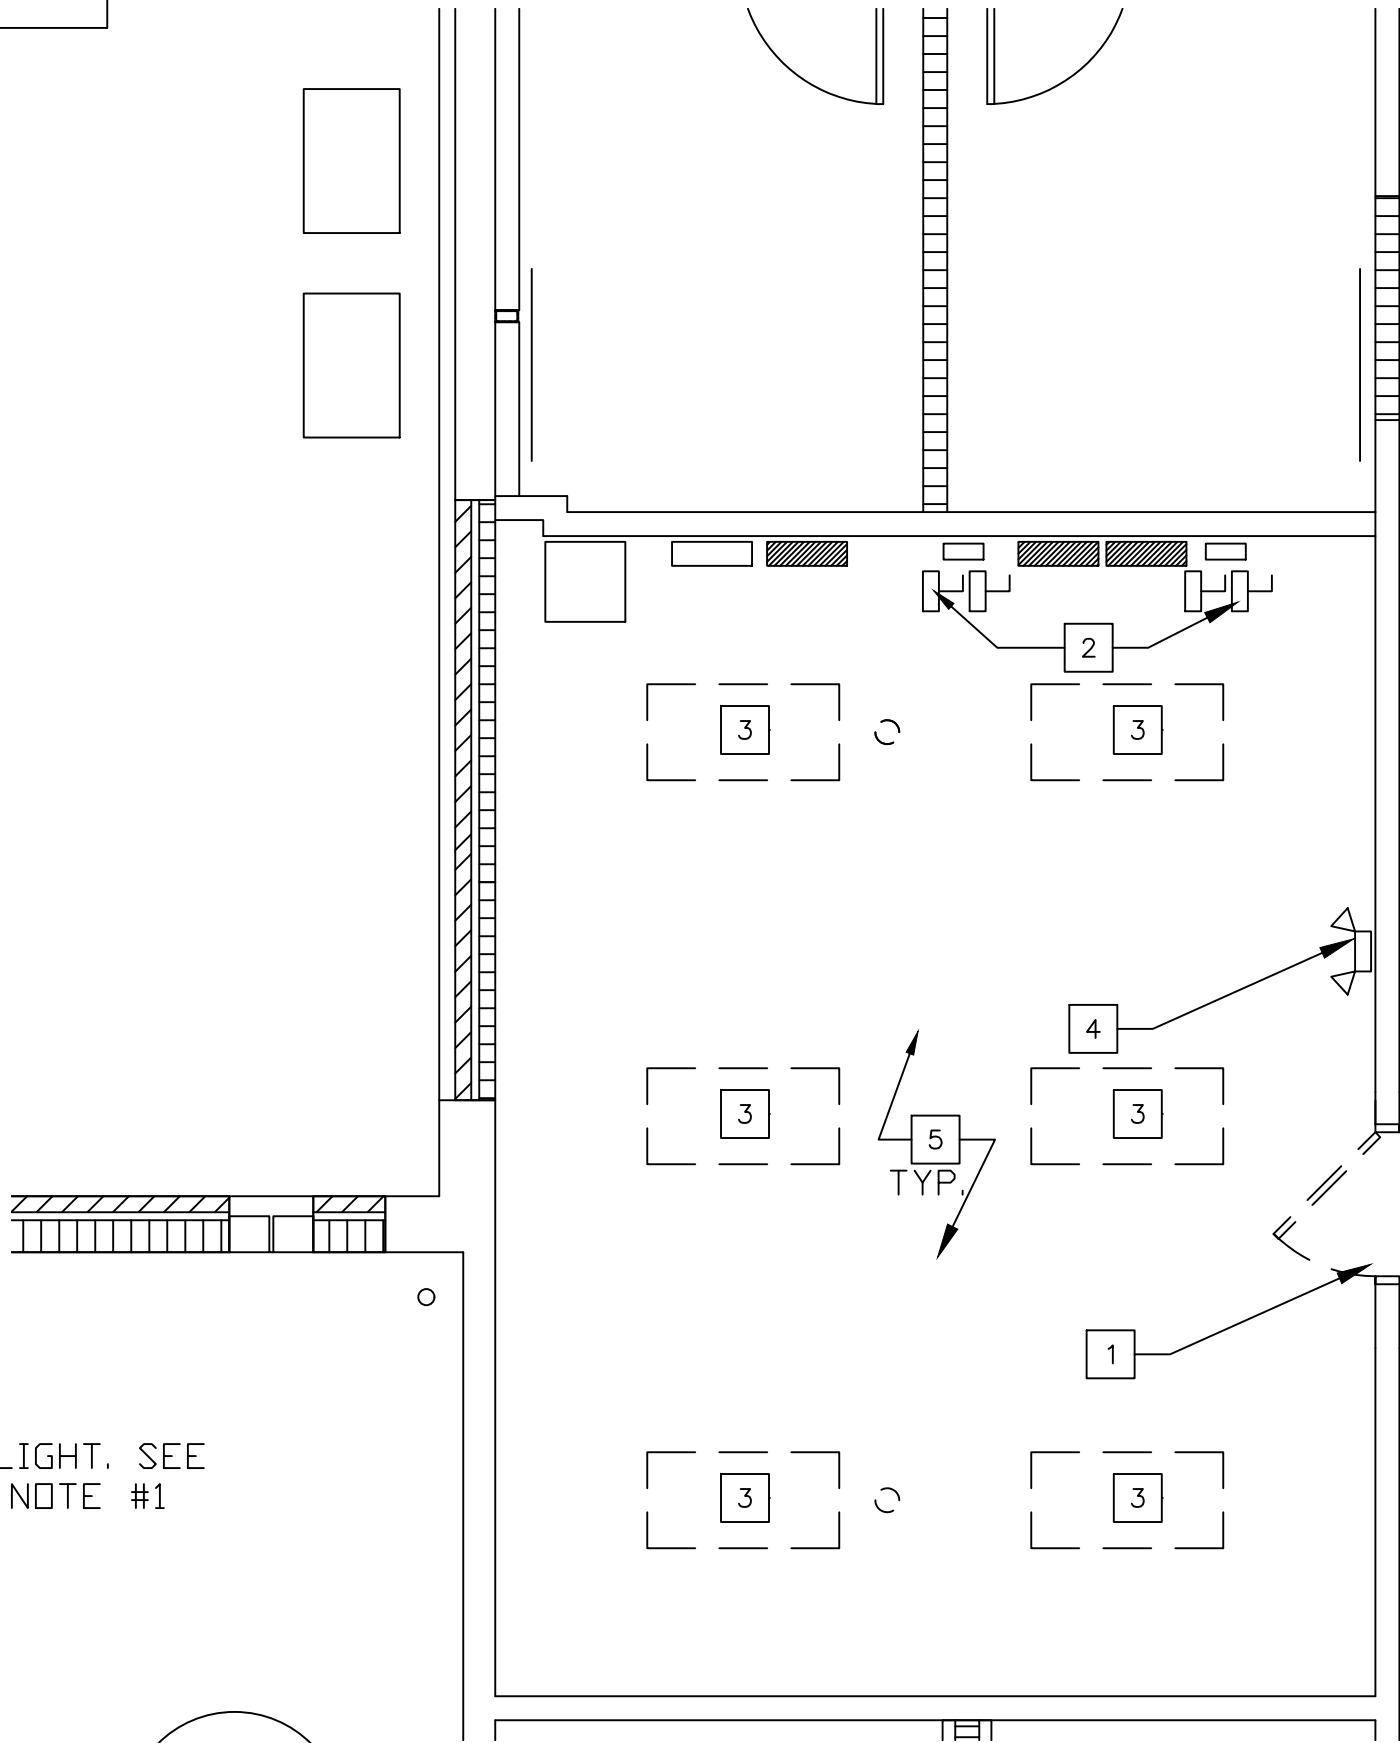

SERVER ROOM ELECTRICAL DEMO PLAN

1/4" = 1'-0" 
