

(SHEETS G-008 AND G-009)

OUTAGE SCHEDULE						
REFERENCE DESIGNATION	TIER	ITEM	PURPOSE	REFERENCE LOCATION/DRAWING	MAXIMUM PERMITTED DURATION FOR EACH OUTAGE	ITEMS AFFECTED BY THE OUTAGE
GENERAL						
G1	TIER 2	PARTIAL ROAD/PARKING	CONSTRUCTION LAYDOWN IN TURNER STREET DURING STRUCTURAL PILE WORK	G-006	6 MONTHS	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
G2	TIER 2	PARTIAL ROAD/PARKING	CONSTRUCTION LAYDOWN AREA ON EAST SIDE OF BUILDING 60	G-006	CONSTRUCTION PERIOD	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
CIVIL						
C1	TIER 2	PARTIAL ROAD/PARKING	SITE WORK IN STORER STREET INCLUDES WATER SERVICE RELOCATION, CONSTRUCTION OF GENERATOR, MECHANICAL PADS, BOLLARDS, REGRADING, AND PAVING.	G-006, CR101, CS101, CG101	1 MONTH	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
C2	TIER 2	PARTIAL ROAD/PARKING	SITE WORK IN TURNER STREET INCLUDES WATER SERVICE RECONSTRUCTION, REGRADING, AND PAVING.	G-006, CR101, CS101, CG101	1 WEEK (OFF HOURS)	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
C3 [OPTION 9]	TIER 2	PARTIAL ROAD/PARKING	OPTION 9: SITE WORK INCLUDES RECONSTRUCTION OF ELECTRIC DUCTBANK IN TURNER STREET FROM LOAD CENTER 4 TO BUILDING 60.	G-006, CR101, CS101, C-201	2 WEEKS (OFF HOURS)	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
ARCHITECTURAL						
A1	TIER 2	PARTIAL ROAD/PARKING	WORK ON THE EXTERIOR OF THE BUILDING INCLUDING WINDOW REPAIR, ROOFING REPLACEMENT, AND MASONRY RESTORATION, WILL REQUIRE ACCESS FROM TURNER ST	G-006, AE100'S, AE200'S	4 MONTHS	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
A2	TIER 2	PARTIAL ROAD/PARKING	WORK ON THE EXTERIOR OF THE BUILDING INCLUDING WINDOW REPAIR, ROOFING REPLACEMENT, AND MASONRY RESTORATION, WILL REQUIRE ACCESS FROM STORER ST	G-006, AE100'S, AE200'S	4 MONTHS	TRAFFIC, FIRE DEPARTMENT ACCESS, AND PARKING
A3	TIER 2	PARTIAL ROAD/PARKING	WORK ON THE EXTERIOR OF THE BUILDING INCLUDING WINDOW REPAIR, ROOFING REPLACEMENTAND MASONRY RESTORATION WILL REQUIRE ACCESS ON THE SOUTH SIDE OF BUILDING 60.	G-006, AE100'S, AE200'S	2 WEEKS	PARKING
	TIER 2					
	TIER 2					
MECHANICAL						
M1	TIER 2	STEAM/HOT WATER	BUILDING 60 STEAM AND HOT WATER SYSTEM ARE BEING REMOVED AND REPLACED.	MD SHEETS	CONSTRUCTION PERIOD	B60 STEAM/HOT WATER SERVICE
M2	TIER 2	STEAM/HOT WATER	BUILDING 60 STEAM AND HOT WATER SYSTEM ONAGE.	M SHEETS	1 DAY (OFF HOURS)	B60 STEAM/HOT WATER SERVICE
	TIER 2					
PLUMBING						
P1	TIER 2	WATER SERVICE	BUILDING 62/62A WATER SERVICE WILL BE TEMPORARILY DISCONNECTED WHILE A PORTION OF BUILDING 60'S WATER SERVICE IN STORER STREET IS REROUTED AND BUILDING 62/62A SERVICE IS RECONNECTED. SEE OUTAGE SCHEDULE NOTE 13.	G-006, CR101, CS101, PD SHEETS	2 WEEK (OFF HOURS)	B62/B2A WATER SERVICE
P2	TIER 2	COMPRESSED AIR	PERMANENT OUTAGE TO UNUSED SERVICE TO B292.	PD SHEETS	PERMANENT	B292 COMPRESSED AIR SERVICE
P3	TIER 2	COMPRESSED AIR	BUILDING 60 COMPRESSED AIR SYSTEM IS BEING REMOVED AND REPLACED.	PD SHEETS	CONSTRUCTION PERIOD	B60 COMPRESSED AIR SERVICE
P4	TIER 2	WATER SERVICE	BUILDING 60 WATER SERVICE ONAGE	P SHEETS		B60 WATER SERVICE
FIRE PROTECTION						
FP1 A WATER B ROAD (TRAFFIC)	TIER 2	HYDRANT FLOW TEST (CONSTRUCTION)	CONDUCT A HYDRANT FLOW TEST AS PART OF THE PROJECT REQUIREMENTS FOR THE SPRINKLER SYSTEMS	FP SHEETS	1-2 HOURS	WATER ROAD/TRAFFIC
FP2	TIER 2	FIRE ALARM	BUILDING 60 FIRE ALARM SYSTEM IS BEING REMOVED AND REPLACED	FD SHEETS	CONSTRUCTION PERIOD	B60 FIRE ALARM SYSTEM
FP3	TIER 2	FIRE SPRINKLER SYSTEM	BUILDING 60 SPRINKLER SYSTEM IS BEING REMOVED AND REPLACED	FP SHEETS	CONSTRUCTION PERIOD	B60 SPRINKLER SYSTEM
ELECTRICAL						
E1	TIER 2	B60 POWER	PROVIDE TEMPORARY POWER PANELS AND TRANSFORMERS TO PROVIDE POWER NEEDED FOR CONSTRUCTION SERVICES AS WELL AS TEMPORARY POWER TO THE EXISTING TRAILERS 1 AND 2. FOR BIDDING PURPOSES, ASSUME REUSE OF EXISTING FEEDER CONDUCTORS, FOR TEMPORARY POWER.	ED101, ED102, ES101, EP501	8 HOURS (OFF HOURS)	B60 POWER EXISTING TRAILERS 1 AND 2 POWER
E2	TIER 2	B74 DC POWER	REMOVE DC POWER CONNECTION BETWEEN BUILDINGS 60 AND 74.	ED102	PERMANENT	B74 DC POWER
E3	TIER 2	B60 POWER	BUILDING 60 ELECTRICAL POWER SERVICE ONAGE	EP102, EP501	8 HOURS (OFF HOURS)	B60 POWER EXISTING TRAILERS 1 AND 2 POWER
E4	TIER 2	B60 EV CHARGING	REPLACE BRANCH CIRCUITS FEEDING THE EXISTING EV CHARGING STATIONS.	ED102, EP102	CONSTRUCTION PERIOD	EV CHARGING STATIONS

(SHEETS G-008 AND G-009)

1. OUTAGES REQUESTED BY THE SCOPE OF WORK INCLUDE, BUT ARE NOT LIMITED TO, THOSE LISTED IN THE OUTAGE SCHEDULE. OUTAGE REQUEST SUBMISSIONS, EXECUTION, AND COORDINATION PERFORMING THE OUTAGES ARE THE RESPONSIBILITY OF THE CONTRACTOR.
2. SUBMIT A WRITTEN OUTAGE PLAN, INCLUDING SEQUENCE FOR OUTAGES AND EXPECTED DURATION OF EACH OUTAGE INCLUDING, BUT NOT LIMITED TO, THOSE LISTED IN THE OUTAGE SCHEDULE. MINIMIZE QUANTITY AND DURATION OF OUTAGES. HIGHLIGHT EACH REQUESTED OUTAGE INDIVIDUALLY ON THE 3 WEEK LOOK AHEAD SCHEDULES. AN APPROVED SCHEDULE AND OUTAGE PLAN ARE REQUIRED PRIOR TO START OF CONSTRUCTION ACTIVITIES.
3. SCHEDULE AND COORDINATE OUTAGES WITH THE CONTRACTING OFFICER.
4. OUTAGES MAY BE SHORT DURATION, LONG DURATION, A PERMANENT REMOVAL OUTAGE, OR REQUEST TO TURN ON/PUT EQUIPMENT INTO SERVICE (A.K.A. AN 'ONAGE').
5. PREPARE A GOVERNMENT FURNISHED OUTAGE REQUEST FORM FOR EACH OUTAGE AND SUBMIT TO THE CONTRACTING OFFICER. TIER 2 OUTAGE REQUESTS NEED TO BE SUBMITTED TO THE CONTRACTING OFFICER A MINIMUM OF THREE WEEKS AHEAD OF THE ANTICIPATED OUTAGE DATE. OUTAGES IDENTIFIED AS TIER 1 IN THE OUTAGE SCHEDULE WILL REQUIRE ADDITIONAL TIME FOR GOVERNMENT REVIEW AND APPROVAL.
6. OUTAGES IDENTIFIED INCLUDE THE CONNECTION TO, OR REMOVAL FROM AN EXISTING UTILITY SYSTEM. AN APPROVED OUTAGE IS REQUIRED FOR CONNECTION TO OR REMOVAL FROM EXISTING UTILITY SYSTEMS. ADDITIONAL OUTAGES MAY BE REQUIRED, DEPENDING ON THE CONTRACTOR'S SCHEDULING SEQUENCING OPERATION, WRITTEN OUTAGE PLAN, AND DIRECTIONS FROM THE CONTRACTING OFFICER, AND THE REQUIREMENTS OF SHIPYARD ACTIVITIES SUPPORTED BY BUILDING 60 UTILITIES.
7. MULTIPLE OUTAGES MAY BE REQUIRED FOR EACH PURPOSE AND/OR WORK ITEM. FOR BIDDING PURPOSES ONLY. MULTIPLE OUTAGES OF THE SAME ITEM MUST BE SEPARATED BY 24 HOURS (MINIMUM).
8. THE MAXIMUM PERMITTED DURATION OF EACH OUTAGE IN THE OUTAGE SCHEDULE IS FOR BIDDING PURPOSES ONLY. THE EXACT OUTAGE DURATION LIMITATIONS WILL BE DETERMINED BY THE CONTRACTING OFFICER.
9. MAJOR SYSTEMS AND FACILITIES AFFECTED BY OUTAGES ARE LISTED IN THE OUTAGE SCHEDULE. THE CONTRACTOR MUST CONFIRM SPECIFICS WITH THE CONTRACTING OFFICER PRIOR TO REQUESTING EACH OUTAGE.
10. AS PART OF EACH OUTAGE REQUEST, INCLUDE REQUESTED GOVERNMENT SUPPORT, REQUIRED GOVERNMENT ESCORTS, TECHNICAL STAFF, SECURITY STAFF, AND SYSTEM OPERATION, TESTING, OR RESTART SUPPORT ANTICIPATED.
11. PROVIDE TEMPORARY SERVICES FOR UTILITIES AFFECTED BY OUTAGES IF THE DESIRED WORK INCLUDED IN THE OUTAGE REQUEST CANNOT BE COMPLETED WITHIN THE MAXIMUM OUTAGE DURATION LISTED AND WHERE SPECIFICALLY INDICATED. PROVIDE TEMPORARY SERVICE/UTILITIES THAT MEET OR EXCEED THE EXISTING SYSTEM'S CAPACITIES. INCLUDE SPECIFIC NARRATIVE DISCUSSION OF THE DESIRED WORK, GOVERNMENT SUPPORT, THE SYSTEMS IMPACTED BY THE OUTAGE, AND A DETAILED DESCRIPTION FOR THE TEMPORARY SERVICE/UTILITY PROVISIONS PROPOSED AS PART OF THE OUTAGE REQUEST. INCLUDE NARRATIVE DISCUSSION OF TRANSITIONS FROM EXISTING SERVICE(S) TO TEMPORARY SERVICE(S) AND RETURN TO EXISTING/INSTALLED SERVICE(S) AS PART OF OUTAGE REQUEST.
12. PRIOR TO EACH OUTAGE, CONDUCT ON-SITE PRE-OUTAGE MEETINGS WITH THE GOVERNMENT AND TRADE TECHNICIANS TO REVIEW THE DETAILS OF THE REQUESTED OUTAGE. THESE MEETINGS ARE A PREREQUISITE FOR APPROVING THE OUTAGE REQUESTS. STATE PROPOSED MEETING DATE/TIME IN EACH OUTAGE REQUEST. FINAL PRE-OUTAGE MEETING DATES AND TIMES WILL BE DETERMINED BY THE CONTRACTING OFFICER.
13. DURING WATER OUTAGES AT BUILDING 60 PROVIDE ELECTRIC WATER COOLER/BUBBLER WITH HOT AND COLD WATER SERVICE AT BUILDING 62A. COORDINATE LOCATION AND FREQUENCY OF REPLACEMENT WATER BOTTLE DELIVERIES WITH THE CONTRACTING OFFICER.
14. STEAM UTILITY OUTAGES MUST OCCUR DURING NON-HEATING SEASON (PROHIBITED SHUTDOWN NOVEMBER THROUGH MARCH).

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

1/23/2026 4:50:21 PM G-009
C:\Users\mdonovan\Documents\22103.25_BLDG60_ARCHITECTURAL-V23_mdonovan8VPXR.rvt

D

C

B

A

OUTAGE SCHEDULE CONTINUED						
REFERENCE DESIGNATION	TIER	ITEM	PURPOSE	LOCATION/DRAWING	MAXIMUM PERMITTED DURATION FOR EACH OUTAGE	ITEMS AFFECTED BY THE OUTAGE
TELECOMMUNICATIONS						
T1	TIER 2	COMMUNICATIONS	BUILDING 60 COMMUNICATIONS NETWORKS (NETWORK N AND P) WILL BE MODIFIED AS PART OF THE BUILDING RENOVATIONS.	ED101, ED102, ET101, ET102, ES101, ET501	CONSTRUCTION PERIOD	B60 COMMUNICATIONS NETWORKS N AND P
T2	TIER 2	TELEPHONES	BUILDING 60 TELEPHONE DISTRIBUTION WILL BE MODIFIED AS PART OF THE BUILDING RENOVATIONS.	ED101, ED102, ET101, ET102, ES101, ET501	CONSTRUCTION PERIOD	B60 TELEPHONE SERVICE EXISTING TRAILER 2 TELEPHONE SERVICE

GENERAL NOTES

1. SEE SHEET G-008 FOR GENERAL NOTE AND OUTAGE SCHEDULE NOTES.




APPROVED	
FOR COMMANDER NAVFAC	
ACTIVITY	
SATISFACTORY TO DATE	
DESIGNER	JMR
DRAWN BY	MJD
CHECKED BY	RSH
DESIGN MANAGER	T. CARLETON
PROJECT MANAGER	L. LYONS
READ/PRIME	
FIRE PROTECTION	S. RUCINSKI

DEPARTMENT OF THE NAVY	NAVAL FACILITIES ENGINEERING SYSTEMS COMMAND
NAVAL FACILITIES ENGINEERING SYSTEMS COMMAND - MID-ATLANTIC	
ROCCC-ME	PORTSMOUTH NAVAL SHIPYARD - KITTEERY, ME
PORTSMOUTH NAVAL SHIPYARD	
B60 REPAIRS	
OUTAGE SCHEDULE CONTINUED	

PROJECT NO.	1740579
NAVFAC DRAWINGS NO.	
SHEET	9 OF 282
G-009	

1/26/2026 2:48:27 PM SB101 C:\Users\mdonovan\Documents\22103.25_BLDG60_STRUCTURAL-V23_mdonovan8\FXR.rvt

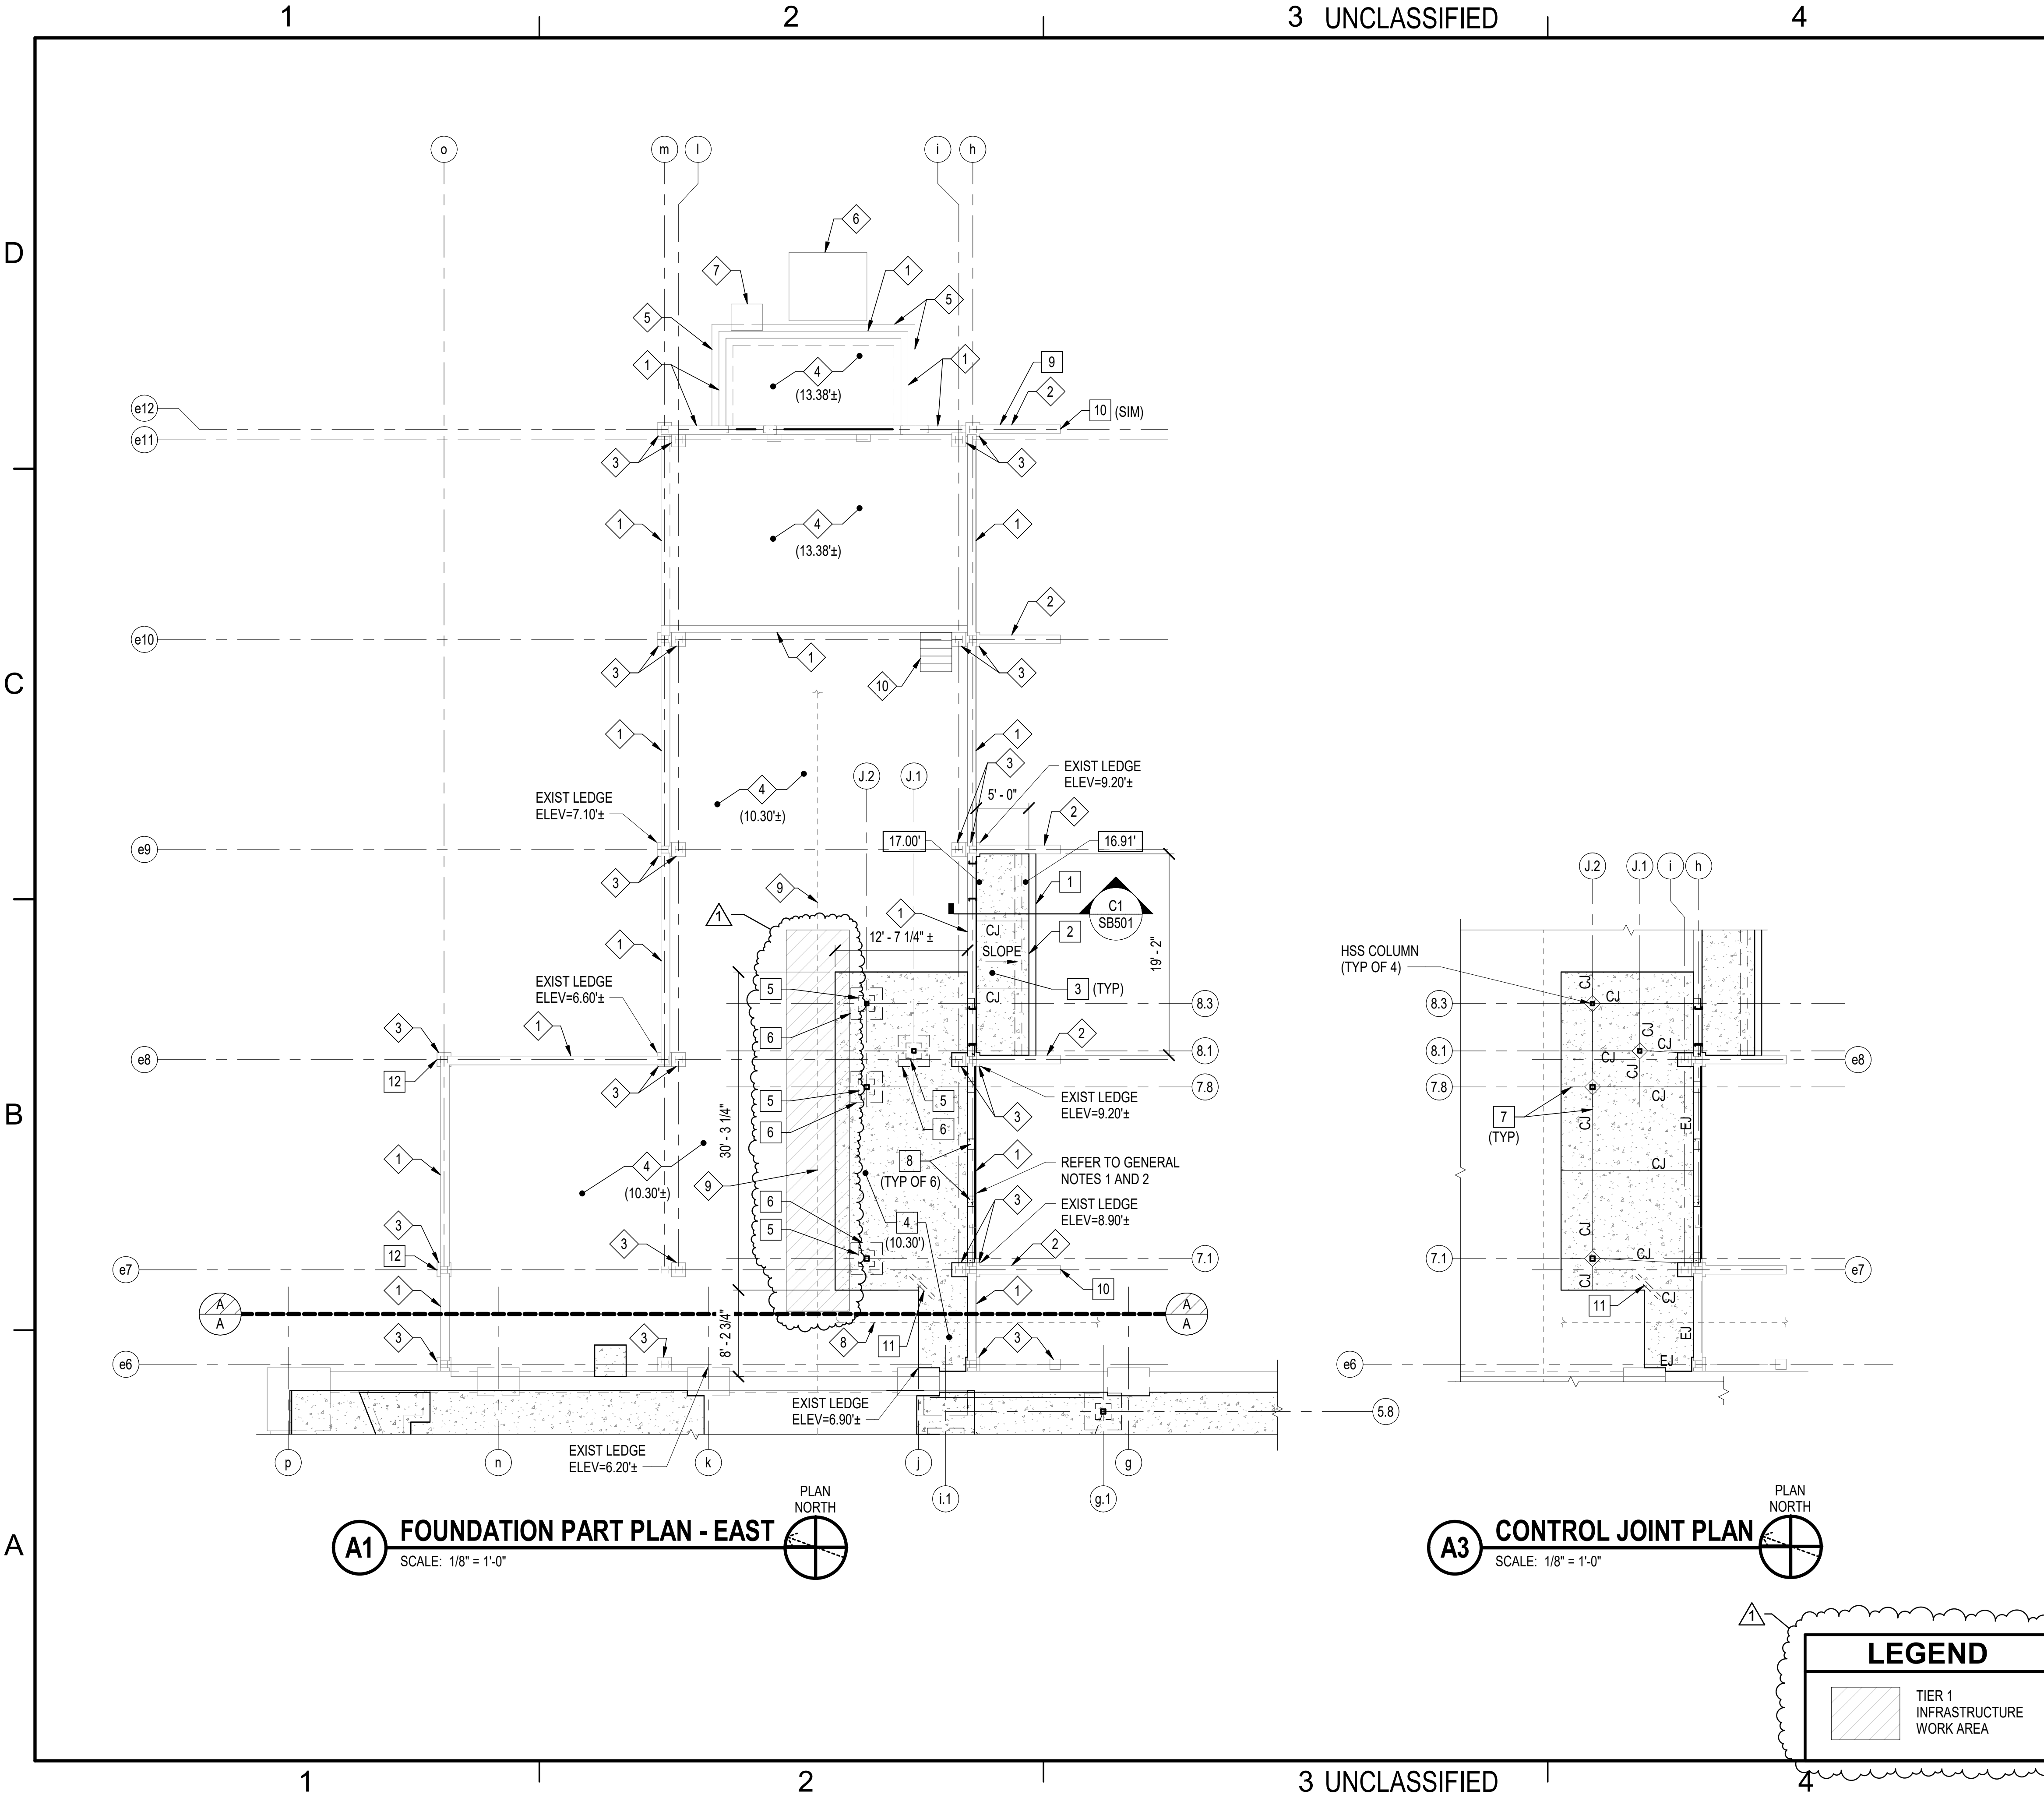

GENERAL NOTES

- REFER TO SHEET CS101 FOR NEW WATER LINE ENTRANCE THROUGH EXISTING FOUNDATION WALL (ABOVE EXISTING SLAB ELEVATION).
- REFER TO ELECTRICAL DRAWINGS FOR NEW POWER LINE THROUGH EXISTING FOUNDATION WALL FOR GENERATOR.
- EXISTING LEDGE ELEVATIONS ARE APPROXIMATE AND ARE BASED ON EXISTING REFERENCE DRAWING 60-51-42.

EXISTING KEYNOTES (THIS SHEET ONLY)

1	EXISTING REINFORCED CONCRETE FOUNDATION WALL.
2	EXISTING REINFORCED CONCRETE BUTTRESS WALL.
3	EXISTING REINFORCED CONCRETE PIER.
4	EXISTING 5"± THICK REINFORCED CONCRETE SLAB-ON-GROUND.
5	EXISTING REINFORCED CONCRETE CONTINUOUS FOOTING.
6	EXISTING REINFORCED CONCRETE EQUIPMENT PAD.
7	EXISTING REINFORCED CONCRETE STOOP PAD.
8	EXISTING STORM DRAIN LINE BELOW SLAB. SEE CIVIL DRAWINGS.
9	EXISTING WATER LINE BELOW SLAB (TIER 1 INFRASTRUCTURE 3- FEET EITHER SIDE OF WATER LINE). SEE CIVIL DRAWINGS.
10	EXISTING STEEL FRAMED STAIRS AND RAILING.

KEYNOTES (THIS SHEET ONLY)

1	1'-0"x2'-0" CONTINUOUS REINFORCED CONCRETE FOOTING.
2	8" REINFORCED CONCRETE FOUNDATION WALL.
3	6" REINFORCED CONCRETE STOOP SLAB WITH BROOM FINISH.
4	5" REINFORCED CONCRETE SLAB-ON-GROUND. DOWEL TO ADJACENT EXISTING SLAB. SEE DETAIL C4/SB502.
5	1'-6"x1'-6" REINFORCED CONCRETE PIER. TOP OF PIER ELEVATION = 9.63'. SEE DETAIL C4/SB502.
6	3'-0"x3'-0"x1'-0" REINFORCED CONCRETE FOOTING ON LEVELING PAD. BOTTOM OF FOOTING ELEVATION = 7.30'. SEE DETAIL C4/SB502.
7	SAWCUT CONTROL JOINT. SEE DETAIL A3/SB501.
8	NON-SHRINK GROUT PAD FOR FIRE PUMP MEZZANINE STEEL BEAMS. SEE DETAIL B3/SB501.
9	OPTION 7: PATCH SPALLING CONCRETE. SEE DETAIL B2/SB502.
10	OPTION 7: REPAIR BUTTRESS END OF WALL. SEE DETAIL A5/SB503.
11	(2) DIAGONAL #5S, 3'-0" LONG, SPACED 4" ON-CENTER AND LOCATED 4" FROM CORNER.
12	OPTION 7: PATCH SPALLING CONCRETE. SEE DETAIL A3/SB502.

KEY PLAN

LEGEND

	TIER 1 INFRASTRUCTURE WORK AREA
--	---------------------------------

GRAPHIC SCALE(S)

1/8" = 1' - 0"

01/27/2026	10/07/2025	DATE
AMENDMENT 004	FINAL SUBMISSION	MARK
1		DESCRIPTION

OAK POINT ASSOCIATES
APPROVED
FOR COMMANDER NAVFAC
ACTIVITY
SATISFACTORY TO DATE
DESIGNER WFG
DRAWN BY MJC
CHECKED BY DNM
DESIGN MANAGER T. CARLETON
PROJECT MANAGER L. LYONS
HEADLINE
FIRE PROTECTION S. RUCINSKI

DEPARTMENT OF THE NAVY
NAVAL FACILITIES ENGINEERING SYSTEMS COMMAND
NAVAL FACILITIES ENGINEERING SYSTEMS COMMAND - MID-ATLANTIC
PORTSMOUTH NAVAL SHIPYARD - KITTERY, ME
PORTSMOUTH NAVAL SHIPYARD
KITTERY, MAINE
B60 REPAIRS
FOUNDATION PART PLAN - EAST

PROJECT NO. 1740579
NAVFAC DRAWING NO.
SHEET 55 OF 282
SB101
DRAWING REVISION: 14 SEP 2023

UNCLASSIFIED

