

VIRTUAL INDUSTRY DAY:

Indian River Lagoon South (IRL-S) Project, C-44 Seepage Management Relief Wells Construction Project

Jacksonville District
1 April 2026

Working Today to Build a Better Tomorrow



US Army Corps
of Engineers®





AGENDA



- **Administrative Items**
- **Presentation (09:00-10:00)**
- **1030-1100 (1st Breakout Session)**
- **1130-1200 (2nd Breakout Session)**
- **1200-1230 (3rd Breakout Session)**
- **1230-1330 (Lunch Break)**
- **1330-1400 (4th Breakout Session)**



ADMINISTRATIVE ITEMS



3

- Phones muted, unless talking, and cameras turned off
- Submit technical questions in writing via ProjNet

<http://www.projnet.org/>

ProjNet review name:

Industry Day - CERP: IRL-S C-44 Seepage Management Feature,
Relief Wells

Quick Add Key is: R3V4PZ-5WFPW8



PRESENTATION TOPICS



- 1) **Project:**
Michael Drog, Project Manager
- 2) **Engineering:**
Crystal Markley, Engineering Technical Lead
- 3) **Construction:**
Victor Guerrero, Resident Engineer
- 4) **Contracting:**
Manuela Voicu, Contracting Officer
Martha Sequeira, Contracting Officer
Ligaya Lowe, Contract Specialist
- 5) **Small Business**



Project Overview






INDIAN RIVER LAGOON - SOUTH

C-44 RESERVOIR & STORMWATER TREATMENT AREA (STA)




6

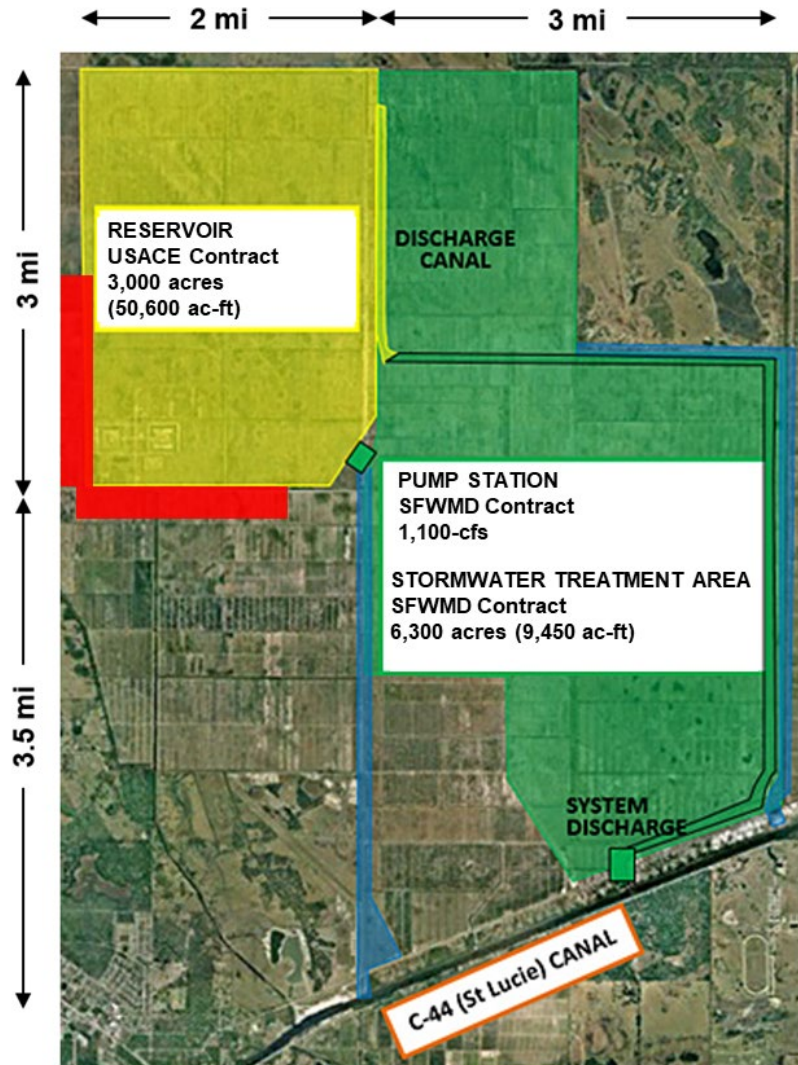

C-44 Reservoir (Corps Construction)

- 50,600 ac-ft of storage, 15-ft depth
- 3,000 acres, 1,100-cfs pump station
- Reservoir final contract acceptance: 13 Nov 2021
- Reservoir Initial Fill: 3 Jan 2022
- Pausing Initial Fill: March 2022
- Design Seepage Management Relief Wells – March 2022 – Jan 2027
- NEW Procurement - Relief Wells - Jan 2027 - May 2027

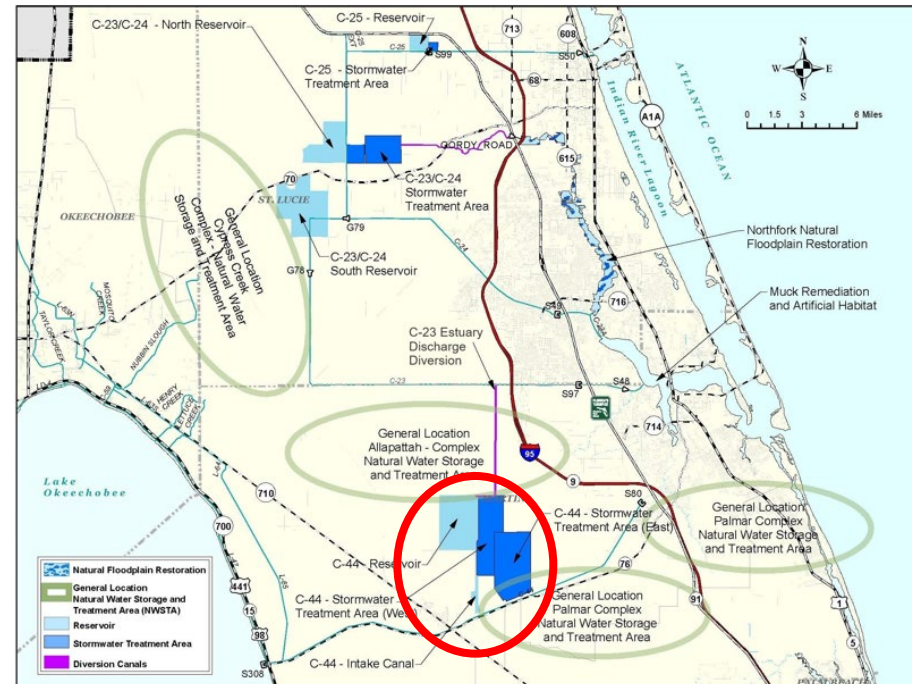

Project Location

Working Today to Build a Better Tomorrow



INDIAN RIVER LAGOON - SOUTH

C-44 RELIEF WELLS PROJECT SUMMARY



Scope (1/2):

- 126 relief wells ~ 50 ft deep.
- Relief well, a 10-inch diameter stainless steel riser and high flow screen, constructed in an 18 to 24-inch diameter pre-drilled borehole.
- Backfill Annulus between the borehole and riser with a uniform and non-calcareous filter media commonly used in the water well industry and selected for compatibility with encountered subsurface materials.
- Above the screen and filter media, the borehole will be sealed with bentonite and grout. All backfill materials will be placed by tremie method.



INDIAN RIVER LAGOON - SOUTH

C-44 RELIEF WELLS PROJECT SUMMARY



Scope (2/2):

- surface protection, access, and discharge features for each relief well.
- Surface & protection feature ~4 ft in diameter and will consist of a standard Florida Department of Transportation Manhole or similar.
- The discharge features will consist of a 12-inch pipe connected to the surface protection and access feature that will terminate at the adjacent canal water level within a concrete headwall.
- Wells tested and accepted no more than 5 days after construction.
- Each outfall construction must be completed no more than 14 days after excavation begins.
- Outfall construction must be completed no more than 60 days after well is completed.



INDIAN RIVER LAGOON - SOUTH

C-44 RELIEF WELLS PROJECT SUMMARY



Location: C-44 Reservoir (directly north of Indiantown, FL)

- Between the perimeter canal and reservoir embankment to relieve pressures as identified during initial operation and testing of the constructed C-44 Reservoir completed in 2021.

Estimated period of performance:

1060 calendar days from receipt of Notice to Proceed (NTP)

Commencement of work:

within 60 calendar days of receipt of the NTP

Corps of Engineers and State of Florida South Florida Water Management District are 50/50 cost share partners



Engineering Overview






AREA OF WORK

Two areas of work:
west side of reservoir
south side of reservoir





AREA OF WORK




Working Today to Build a Better Tomorrow




AREA OF WORK

- **Construction access** from Citrus Blvd, through the Pump Station to access the perimeter road on the south and west of the reservoir

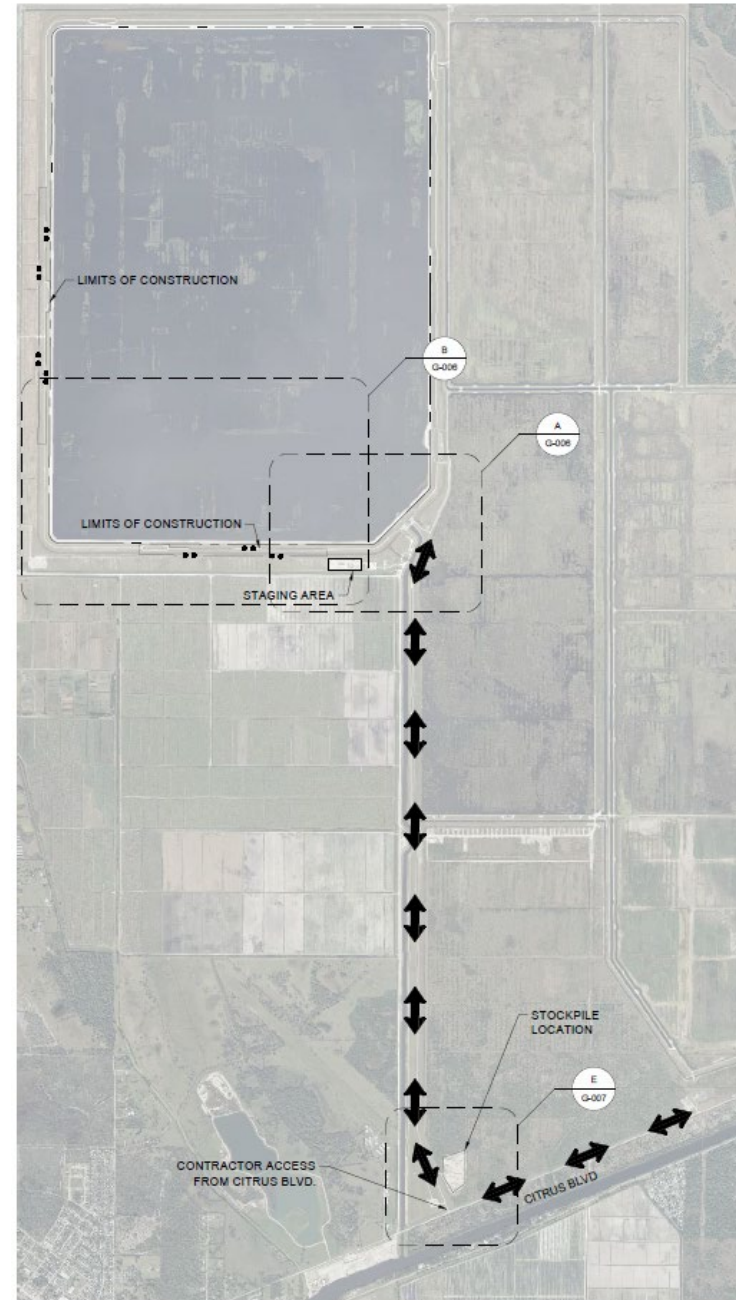




AREA OF WORK



Working Today to Build a Better Tomorrow



AREA OF WORK-WEST

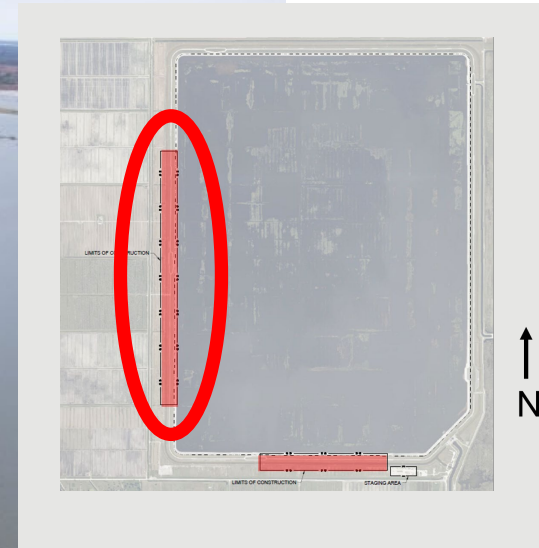

Working Today to Build a Better Tomorrow



AREA OF WORK-SOUTH



16




↑
N

Working Today to Build a Better Tomorrow





RELIEF WELL DESIGN

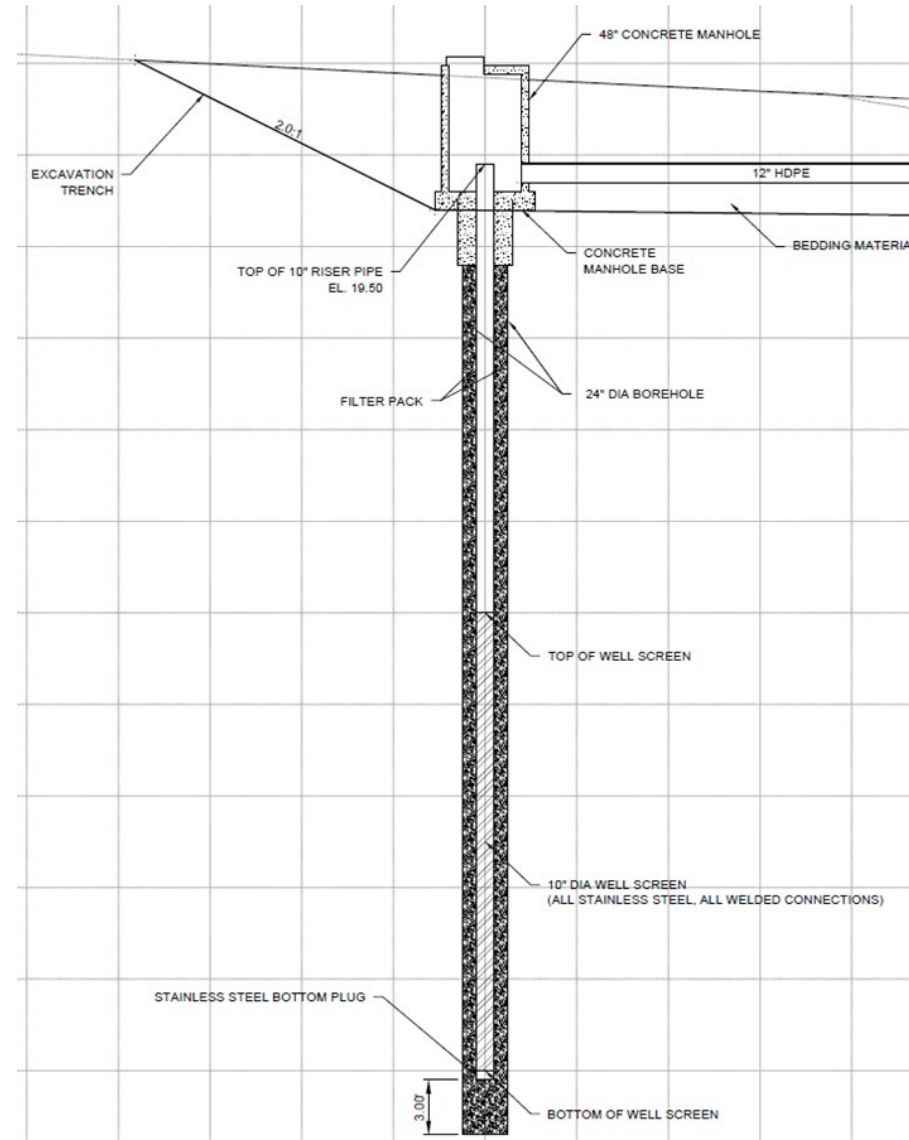




RELIEF WELL DESIGN

- All well pipe is 10" Ø Stainless Steel
- Top of Riser Elevation is constant
- Top of Grout is constant
 - Grout thickness is variable 3 ft. min
- Bentonite thickness is constant
- Well Screen and Filter Pack dimensions vary by well
- Screen: Continuous Wire Wrap, Stainless Steel
- Filter Pack: Uniformly Graded Quartz Sand, typical of water well industry
- Welded Stainless Steel plate to plug bottom of well
- Total Depth ~ 50 – 60 feet Below Ground Surface



OUTFALL SYSTEM DESIGN


- Relief well protected inside 48 in concrete manhole
- 12 in HDPE pipe carries water to WRPC
- Pipe invert elevations are constant
- Distance from relief well to WRPC varies

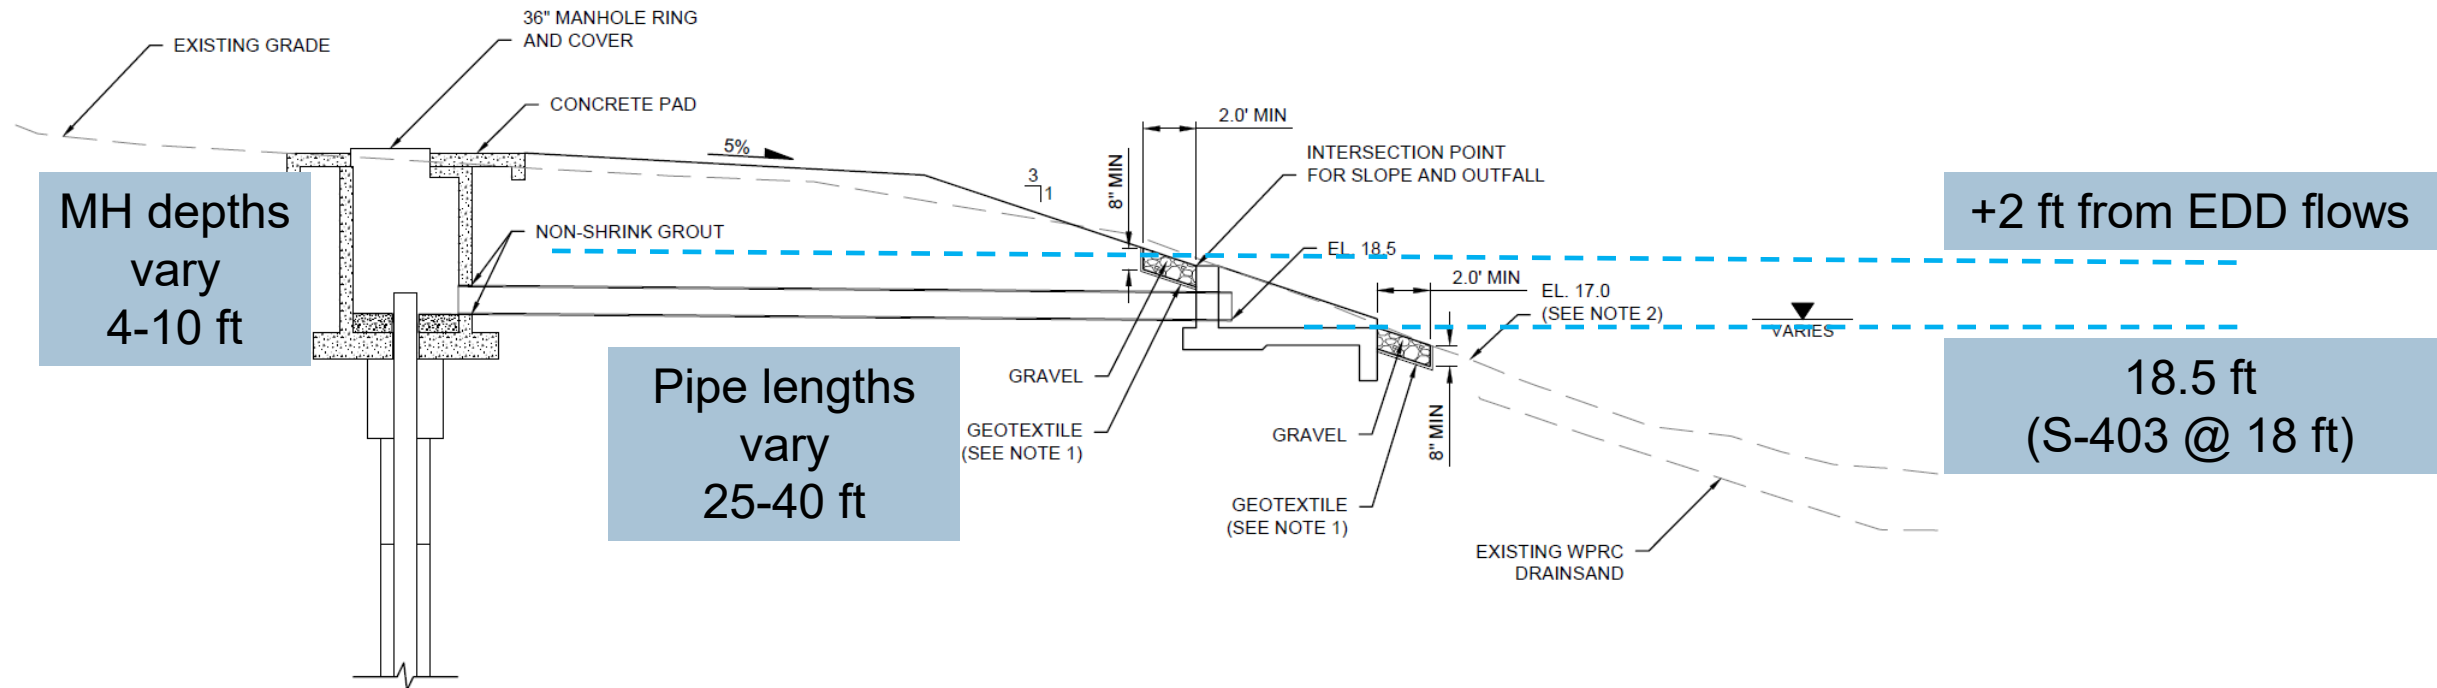



RELIEF WELL SPACING


- Relief wells will be installed at pilot hole locations, 50 ft spacing typical

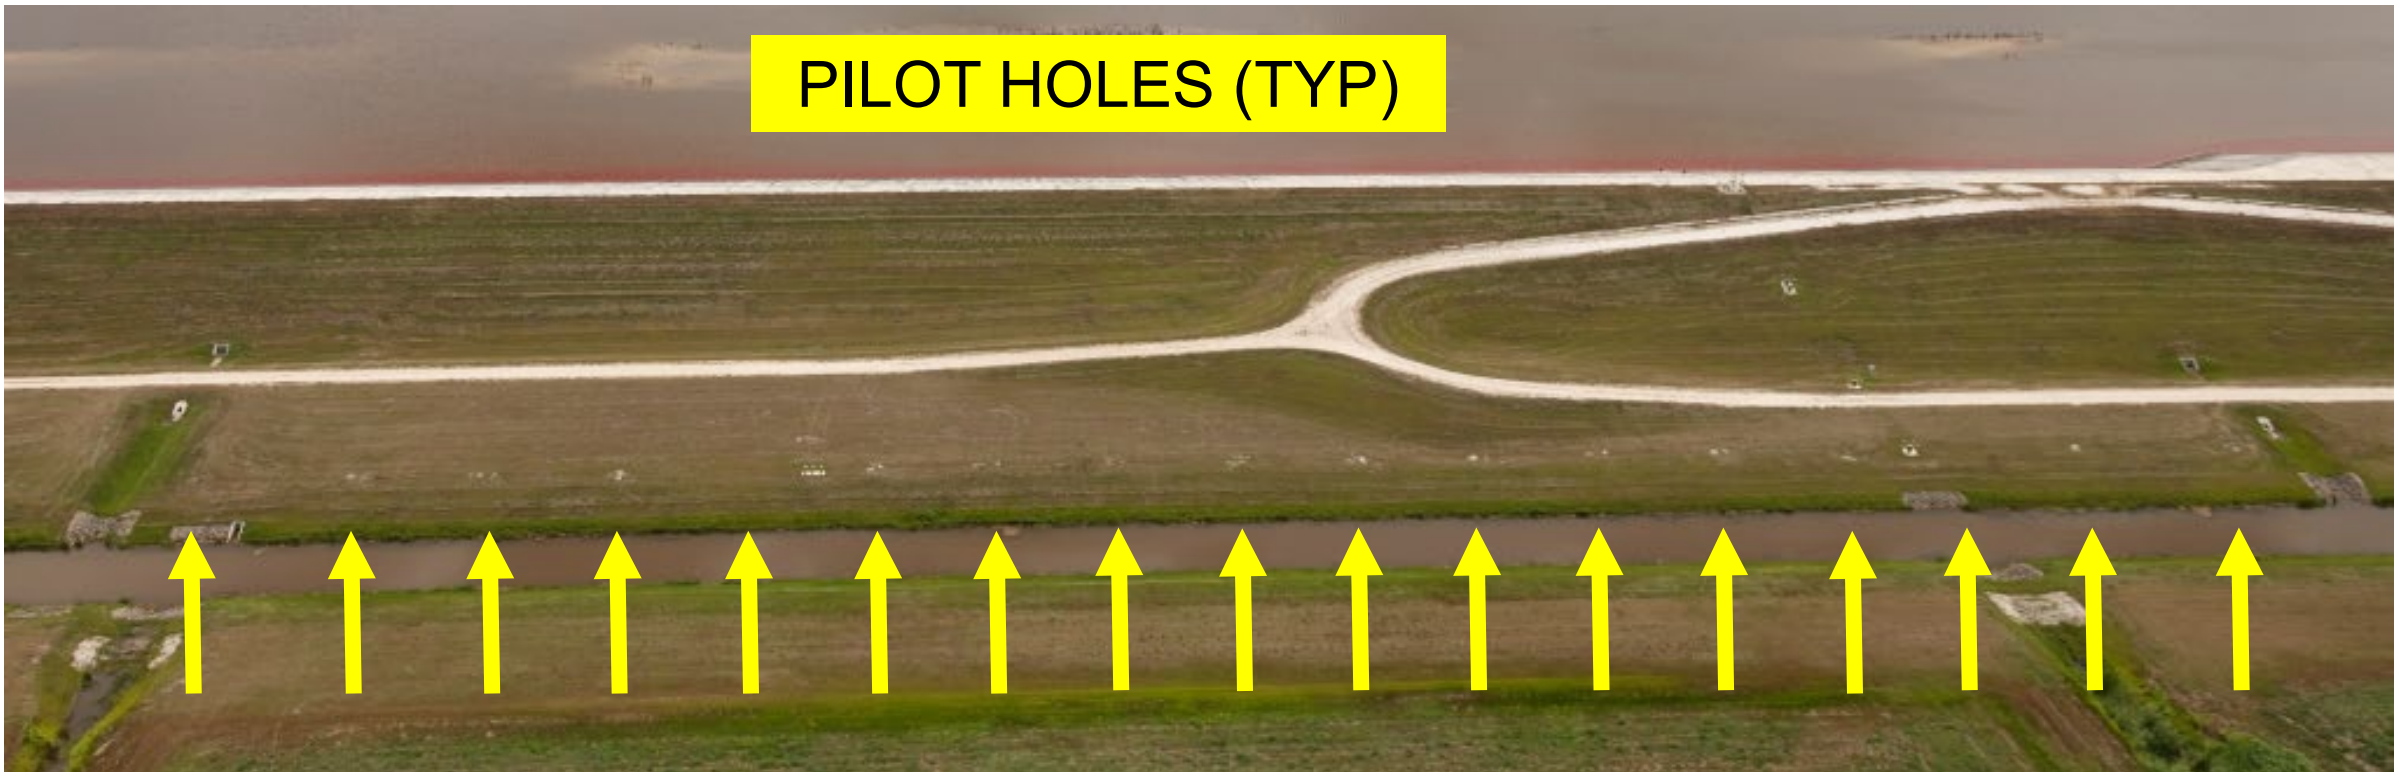



OPERATIONAL CONSTRAINTS

- Operational considerations during construction:
 - Reservoir operations will not be limited, assume 3-10 ft reservoir pool for entire contract
 - Estuary Diversion Discharge (EDD) operations will not be limited, assume 0-2 ft additional stage in WRPC for entire contract

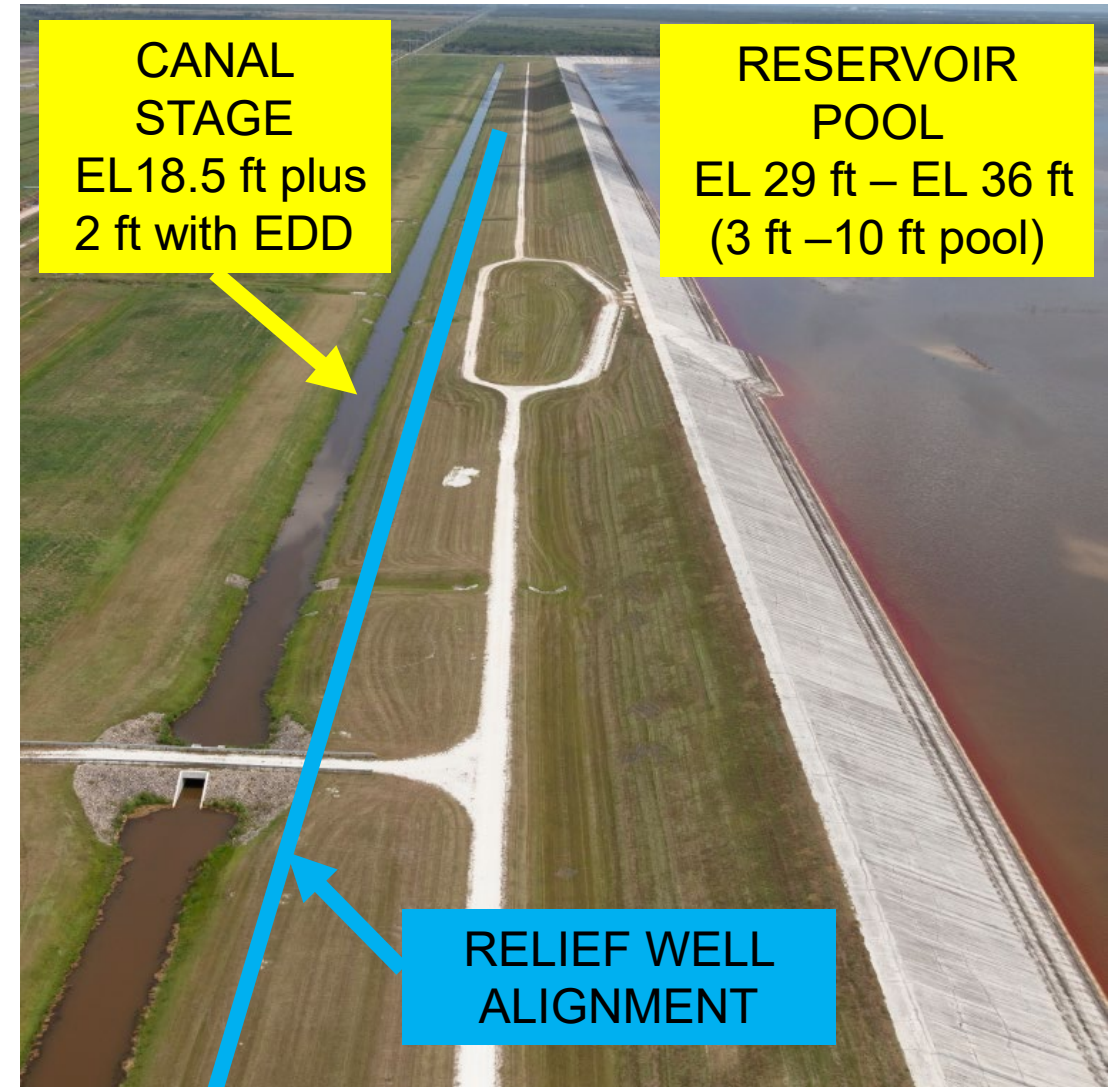



Construction Overview





INDIAN RIVER LAGOON - SOUTH C-44 RELIEF WELLS



- **Construction Quality Control** 3 – phase construction
- **Documentation Requirements**
 - ▶ Submittals
 - ▶ Certifications
 - ▶ Certified Payrolls
 - ▶ COIs
- **Important to USACE**
 - ▶ Data Management
 - ▶ Surveying
 - ▶ QCing of submittals
 - ▶ QA Testing



ADDITIONAL RESOURCES



Construction Quality Management for Contractors (CQM-C) Course:

<https://www.saj.usace.army.mil/About/Divisions-Offices/Construction/CQMC-Course/>

- ▶ Course **required** for CQC Managers & Alternates
Specification 01 45 05 - Contractor Quality Control.
- ▶ Certificate good for 5 years

EM 385-1-1 Safety Manual:

<https://www.publications.usace.army.mil/USACE-Publications/Engineer-Manuals/>

- ▶ Government Safety requirements
Specification 01 35 26



Contracting Overview





CONTRACTING POINT OF CONTACTS

Manuela Voicu, Contracting Officer

Email: Manuela.D.Voicu@usace.army.mil

Martha Sequeira, Contracting Officer

Email: Martha.G.Sequeira@usace.army.mil

Ligaya Lowe, Contract Specialist

Email: Ligaya.M.Lowe@usace.army.mil



ACQUISITION APPROACH

- ▶ Acquisition Approach is still being developed.
- ▶ FAR Part 15 - Contracting by Negotiation. Request for Proposal.
- ▶ Best Value Continuum.
- ▶ FAR 15.002(b) – Competition Acquisitions.
 - Tradeoff Process (FAR 15.101-1)
 - Lowest Price Technically Acceptable source selection process (FAR 15.101-2)



GENERAL INFORMATION



- ▶ **Estimated Period of Performance:**
1060 calendar days from Notice to Proceed (NTP) date
commencement of work within 60 calendar days of NTP receipt.
- ▶ **Type of contract:** Firm-fixed-price
- ▶ Applicable North American Industry Classification System (NAICS)
code assigned to this procurement is 237990, Other Heavy and Civil
Engineering Construction.
The Small Business Size Standard for this project is \$45.0 million.
- ▶ **Subcontracting Plan** is required from Other than Small Business Firms
(FAR Part 19).



GENERAL INFORMATION

- ▶ All information for this project will be posted on:
Systems for Award Management - www.sam.gov and/or
Procurement Integrated Enterprise Environment - <https://piee.eb.mil/>
- ▶ PIEE will be the only authorized transmission method of proposals in response to the solicitation, once issued.
- ▶ Eligibility: **SAM registration required** to receive an award from any Government solicitation.
- ▶ A Sources Sought Notice **W912EP26X1B5D** was posted via SAM.gov on 2 February 2026. Response date was 26 February 2026.
- ▶ Industry Day Notice **W912EP26Z1BBR**. Posted on 10 March 2026. Information included on how to submit questions via ProjNet for this project. All **questions and feedback due 5:00 pm, EDT Wed, 8 April 2026**



TENTATIVE MILESTONES SCHEDULE

Pre-solicitation:	(January 2027)
Advertisement:	(February 2027)
Proposals Due:	(March 2027)
Award Date:	(May 2027)

(Dates are estimates)



Small Business Overview





SMALL BUSINESS OPPORTUNITIES

Alexandria Lavey, Presenter

Kimberly Daniel-Ray, Deputy Small Business

Email: Kimberly.S.DanielRay@usace.army.mil

Phone: (904) 232-1150





SMALL BUSINESS OPPORTUNITIES

- **FAR 19.201 – Government policy**

(a) It is the policy of the Government to provide maximum practicable opportunities in its acquisitions to small business, veteran-owned small business, service-disabled veteran-owned small business, HUBZone small business, small disadvantaged business, and women-owned small business concerns. Such concerns must also have the maximum practicable opportunity to participate as subcontractors in the contracts awarded by any executive agency, consistent with efficient contract performance.

- Small Business Participation
- Subcontracting Plan (other than small business concerns only)

- **DFARS 215.304(c)(i) – Evaluation factors and significant subfactors**

In acquisitions that require use of the clause at FAR 52.219-9, Small Business Subcontracting Plan, other than those based on the lowest price technically acceptable source selection process (see FAR 15.101-2), the extent of participation of small businesses to include service-disabled veteran-owned small business concerns, HUBZone small business concerns, small disadvantaged business concerns, and women-owned small business concerns in performance of the contract shall be addressed in source selection. The contracting officer shall evaluate the extent to which offerors identify and commit to small business performance of the contract, whether as a joint venture, teaming arrangement, or subcontractor.



SMALL BUSINESS SUBCONTRACTING PLAN VS. SMALL BUSINESS PARTICIPATION PLAN



Small Business Participation Plan/ Commitment Document <u>EVALUATION</u>	Subcontracting Plan <u>ASSESSMENT</u>
FAR 15.304, DFARS 215.304	FAR 19.704
Solicitation establishes requirements and evaluation criteria for SB participation	Must be assessed and determined acceptable by the Contracting Officer
Evaluation conducted IAW solicitation evaluation criteria	Must have 15 items defined in FAR 52.219-9
Required only for certain DoD-negotiated acquisitions	Required for all Federal contracts with applicable dollar values (subject to limitations and exceptions) and includes both negotiated and sealed bidding
Applies to ALL businesses	DOES NOT apply to Small Businesses
Can be based on anticipated subcontracting dollars or Total Contract Value (TCV) TCV preferred	Based on total planned subcontracting dollars

NOTE: Both are contractually binding.



MAXIMUM PRACTICAL OPPORTUNITY

- Breaking out contract work requirements
- Performing market research
- Solicit early and allow sufficient time to respond
- Mentor-protege program
- Advertising subcontracting opportunities
- Davis-Bacon prevailing wage rates is a FAR (contract) requirement
- Reach out to the APEX Accelerators, SBA, local state offices and other sources for assistance



PROCUREMENT ASSISTANCE



SB Resources

- Business Opportunity Specialist (SBA)
- Procurement Center Representative (SBA)
- APEX Accelerators

Marketing Resources

- Contract Opportunities on SAM.gov
- Dynamic Small Business Search System
- Forecast of Contracting Opportunities

Other Resources

- USASpending
- DoD Prime Contracting Directory



SMALL BUSINESS OFFICE POINTS OF CONTACT



Kimberly (Kim) Daniel-Ray,
Chief of Small Business Programs
USACE, Jacksonville District
Mobile: (904) 318-6436
Small Business Email: **SAJ-
SB@usace.army.mil**

Alexandria Lavey,
Small Business Professional
USACE, Jacksonville District
Office (904) 232-1005
Small Business Email: **SAJ-
SB@usace.army.mil**



CLOSING REMARKS



38

- Break-Out Sessions Transitions
- Submit technical questions in writing via ProjNet

<http://www.projnet.org/>

ProjNet review name:

Industry Day - CERP: IRL-S C-44 Seepage Management Feature,
Relief Wells

Quick Add Key is: R3V4PZ-5WFPW8

All questions and feedback due 5:00 pm, EDT Wed, 8 April 2026
