

ATF Agile Playbook

Purpose

Agile, an inclusive term that describes a methodology, is a set of development and project management practices that focuses on scope flexibility, team empowerment, continuous improvement and delivering essential quality products in a shorter time span. It is based on iterative and incremental development, where requirements and solutions evolve through self-organized and collaborative cross-functional teams.


Agile methodologies include Scrum, Kanban, Extreme Programming (XP), and Lean, among others. These methodologies all focus on people, communications, the product, and flexibility in order to satisfy customers through early and continuous delivery of valuable solutions. By selecting a shortened duration of time to focus on a finite list of requirements, a delivery team can work to rapidly develop and test solutions thereby reducing the risk of developing solutions based on stale, outdated or miss-understood requirements. By delivering frequently, increased visibility into the progress of the solution is brought forward resulting in a more effective means of measuring successes and deviations.

The purpose of these series of pages is to provide guidance for teams who are engaging in ATF Agile projects, outlining the practices and artifacts that are generally expected by project teams using the ATF Agile methodology. This document covers the project from Discovery/Sprint 0 through the Release Integration testing that typically occurs in the TEST/IVV environment. This content is intentionally maintained on SharePoint to easily facilitate updates as best practices are identified and adopted within ATF.

Execution

Process that ATF uses to develop, build or deploy products.

ATF has adopted a Scrum based processes that has been refined to account for ATF's unique needs. The process is iterative and working product is built to show value and solicit feedback on a frequent basis.

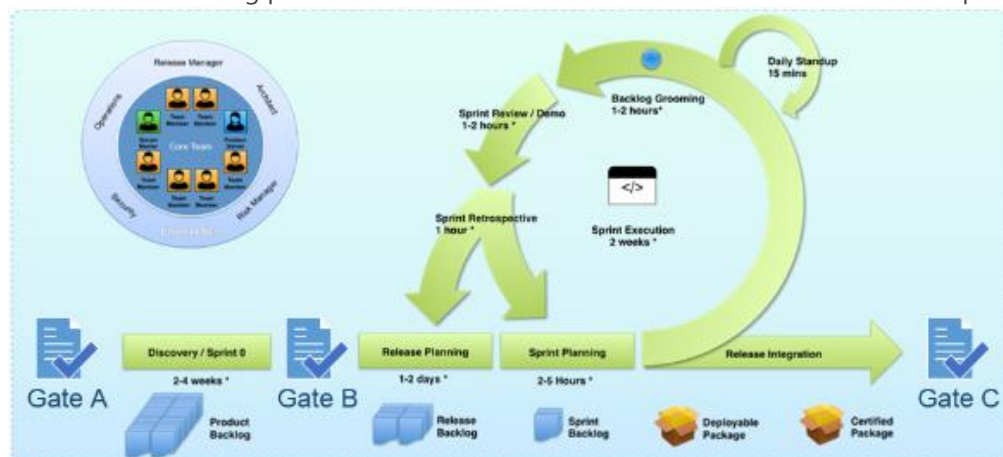


For more information on other work path types, refer to the [PMO's SharePoint](#)

Format

The process is documented within the SharePoint sites listed above. Each page contains the same structure for continuity.

Time Box, Roster and Goal	
Time Box	Discovery / Sprint 0 is expected to take this long to complete: Typically this period may last from 2-4 weeks, but could be longer depending on the project. The Discovery Period / Sprint 0 is over when the team can begin to build the product.
Roster	These individuals and groups are expected to take part in Discovery / Sprint 0: - Core Scrum Team - Product Owner - Scrum Master - Team Members: Developers, Testers, Engineers, (whoever is building the product), etc. - Domain Subject Matter Experts - Information Systems Security Officer - Enterprise Architectural Engineers - End Users - Functional Subject Matter Experts - Anyone other stakeholder who will contribute to requirements gathering and preparing the Core Scrum Team to build
Goal	This is the goal of Discovery / Sprint 0: - To familiarize the team's understanding of the process and product to be developed. - To discover the product's requirements and establish the initial Product Backlog that will be continuously refined as the project progresses and product is incrementally developed and delivered.

Inputs, Processes and Outputs	
Inputs	These inputs are expected to be available in order to begin the Discovery / Sprint 0: - Identified Core Scrum Team (development team) - ATF Agile Training materials
Process	These activities are expected to take place during the Discovery / Sprint 0 session(s): - Kickoff Meeting for Scope and Admin Items Attendees: Product Owner, Scrum Master, Stakeholders Outcome: Identification of Project Vision, desired skillsets, logistical items (seating, software, infrastructure) Benefit: Scope is clarified for all parties to ensure everyone is in the correct mindset and clear on the overall mission - Training Session(s) Attendees: Product Owner, Scrum Master, Team Members Outcome: Consistent understanding of the ATF Agile process and terminology. Benefit: Initial Agile/Scrum Training to level set team members to understand the process - Sticky Session(s) to identify User and High-Level functionality Attendees: Product Owner, Scrum Master, Identified Team Members and Subject Matter Experts Outcome: Logical set of Users and high-level elements of functionality to be delivered during the execution of the project Benefit: Many team members contribute to creation of initial Product Backlog to cover proper breadth and depth, with these notes as a foundation for User Stories - Story Writing Session(s) Attendees: Product Owner, Scrum Master Outcome: Initial set of User Stories and Acceptance Criteria created by Product Owner and supported by Scrum Master Benefit: Product Owner references sticky note groups identified in previous session to create first User Stories - Review Session(s) Attendees: Product Owner, Scrum Master, Team Members Outcome: Team Member understand initial set of User Stories after discussion with Product Owner

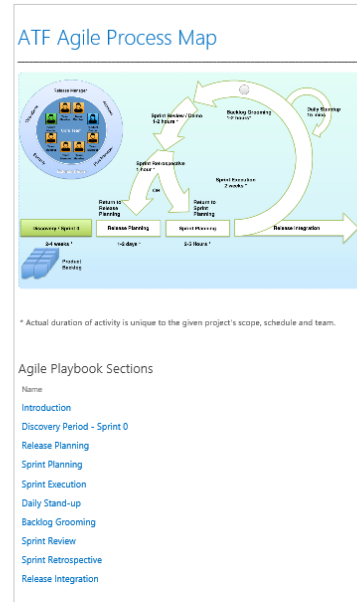

Agile Playbook Sections

Name

Introduction

Discovery Period - Sprint 0

Release Planning

Sprint Planning

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Discovery Period/Sprint 0 Discussion Board

+ new discussion

Recent My discussions Unanswered questions ...

There are no items to show in this view of the "Discovery Period - Sprint 0 Discussion Board" discussion board.

In the Center column:

- Time box** The duration an activity is suggested should take place.
- Roster** The participants that are suggested to be included in the activities.
- Goal** The intended outcome or purpose for the activity.
- Inputs** The expected materials and/or resource needed to complete the activities.
- Process** The list of tasks and processes to be executed within the activity.
- Outputs** The expected materials and/or resources expected as an outcome.
- Other** Anything else that needs to be taken into account during this section of the process.
- Next Step(s)** Identifies what the next step would likely be.

In the Right column:

ATF Agile

Process Orients the viewer on where in the lifecycle they are.

Map

Agile

Playbook Provides the viewer quick links to different sections in the process.

Sections

Discussion Provides the viewer the ability to provide feedback or review other's feedback on the
Board current section of the process.


Core Team

This is the team that is ultimately responsible for developing, testing and delivering the product increments each sprint. This team is a cross-functional group of professionals with the required skills to get the incremental functionality delivered. This is a dedicated team that works together sprint over sprint and from project to project. The core team members of any scrum team are:

1. Product Owner and/or PO Proxy and/or BA
2. Scrum Master
3. Development team which typically constitutes a mix of Developers and Testers

Typically this team should not exceed 9 members.

- 1 PO/Proxy
- 1 Scrum Master
- 3-4 Developers
- 2-3 Testers

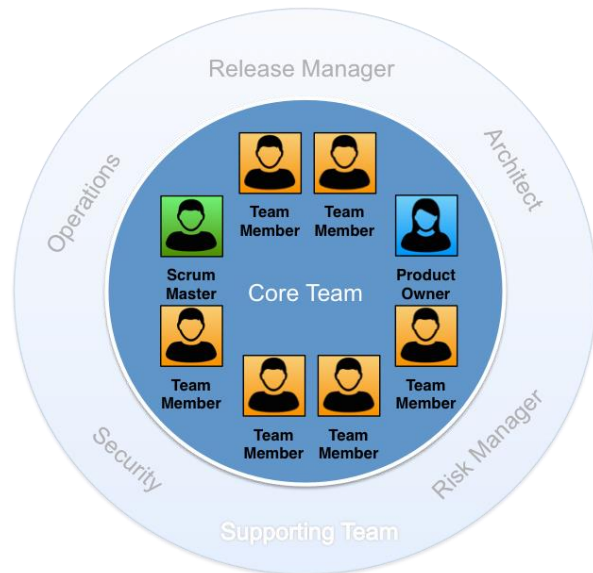

Business Analyst

Supporting role to a Product Owner to help document User Stories and Acceptance Criteria.

- Generate User Stories under the direction of the PO.
- Update User Stories under the direction of the PO.
- Act as a liaison between the PO and the core team.
- Attends the meetings on behalf of the PO (except demo) but frequently is just a go between to get questions the core team has answered by the PO.

Developer

A product builder who specializes in coding the software that meets stated acceptance criteria

- Build the product.
- Contribute to the development of User Stories.
- Contribute to the development of a Sprint Backlog / Plan.

Product Owner

The Product Owner is the single point of contact for the Team regarding the product that is to be built. The PO identifies priority and filters stakeholder requirements and feedback into User Stories for the team to deliver. The PO is an integral part of the Scrum delivery team and is called upon repeatedly to clarify points of interest or contention during the development cycle.

- Write User Stories
- Prioritize and Order the Product Backlog
- Available to the team to provide clarification during Sprints to maximize performance and output

[Product Owner Proxy](#)

The Proxy Product Owner assumes the responsibilities of a Product Owner without the authority, serving in the role expected of the PO, but always clarifying and/or confirming decisions with the PO.

- Write User Stories, Acceptance Criteria (*confirm with PO for accuracy*).
- Provide daily feedback and direction to the team (*confirm with PO as necessary*).
- Order User Stories in the Backlog (*confirm with PO as necessary*).

It is important to note that the Proxy should have sufficient Subject Matter Expert (SME) knowledge to be able to respond to the majority of the teams' questions without having to see the PO for input. If the Proxy has to follow up with the PO with too many questions then the implementation of a Proxy becomes counterproductive, adding an additional layer of communication and an impediment, as they are now a go-between.

[Scrum Master](#)

The Scrum Master (SM) is a servant leader who is primarily responsible to facilitating the processes involved in a Scrum delivery team. The SM ensures the team stays productive by identifying and removing impediments thus allowing the scrum team to stay focused on delivering product.

Remove Impediments

The SM nurtures the team's self-organization and ensures any distractions, impediments, or roadblocks are eliminated. These can be external to the team (i.e. lack of support from another team), or they could be internal.

Coach the team

The SM goal is to increase the team's performance through coaching and training. The SM will help the PO understand how to create and maintain the Product Backlog. The SM ensures the team meets the acceptance criteria defined by the PO and the definition of done created by the team.

Coach the organization

The SM ensures that the Scrum practices and principles are understood not only internally to the team but also externally to rest of the organization. They help those outside of the Scrum team understand the process and principles and how their teams should interact with the Scrum team(s) so it provides value to the team and not an impediment to create product.

[Team Member](#)

Team Members are the product builders. Team Members are made up of various skills and experience.

- Develop and Test the product
- Participate in the development/refinement of User Stories
- Identify the complexity of User Stories
- Build the Sprint Plan (tasks associated with a Sprint Backlog)

Tester


A product builder who specializes in testing the product meets stated acceptance criteria.

- Test code.
- Contribute to the development of User Stories.
- Contribute to the development of a Sprint Backlog / Plan.

Supporting Team

While the "Core Team" is ultimately responsible for the development and testing of the functionality there are other organizations/teams that have to provide support during each sprint. These people are typically only needed sporadically during a sprint and thus may support several teams. This can include (but not be limited to

- Subject Matter Experts (SME)
- System & Data Architects
- Database Administrators (DBA)
- Configuration Management
- Operations/Environment Management
- Documentation & Training organizations
- Release level testing teams (Integrated & Performance)
- Information Systems Security Officer

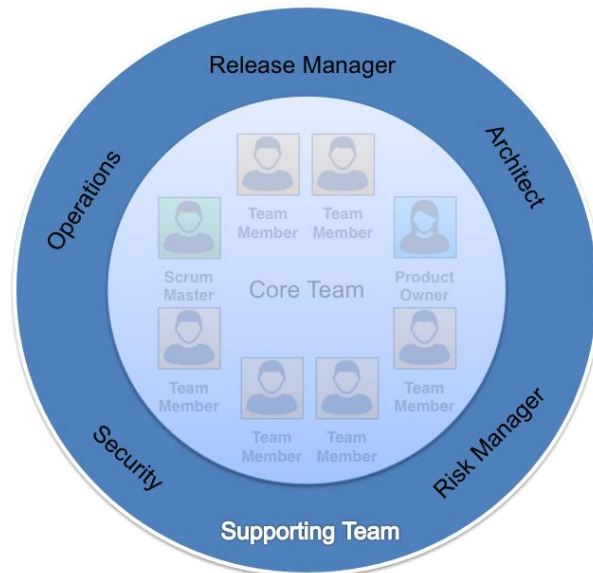

Configuration Management

- Advisory role for Configuration Management compliance, documentation and processes.
- Provide guidance on the CM submission process within Dimensions.

Contracting Officer's Representative

- Monitor and inspect vendor performance and deliverables.
- Ensure adherence to SOW requirements and responsibilities.
- Provide vendor with required access, equipment, and tools to conduct all activities under the contract.

Database Administrator

- Advisory role for knowledge transfer with previous efforts and legacy systems.

ATF Agile Playbook and Agile Tool Suite

- Assist the project team in making informed decisions for legacy database connections and interfaces.

Information Systems Security Officer

- Serve as the subject matter expert on DOJ and ATF Security Policy.
- Conduct security testing and assessment toward System Certification and Accreditation activities.
- Contribute security related acceptance criteria for appropriate user stories.
- Review technical design and architecture to ensure compliance to applicable standards.
- Advise the project team on security related requirements, design and documentation.

Line of Business SME

- Provide subject matter expertise for the line of business being addressed by the product and the Core Team.
- Contribute to user stories and acceptance criteria.
- Contribute in testing developed functions against the pre-defined and agreed upon user stories.
- Advise Product Owner in setting priorities.
- Advise Product Owner in documenting defects.

Managed Services Provider Representative

- Serve as a primary point of contact for the Managed Services team.
- Facilitate coordination of activities between the project team and infrastructure support teams.
- Identify and plan for resource needs in operations and maintenance life cycle stage.

Operations Team POC

- Serve as the Core Team's primary point of contact on the Operations Team.
- Resource planning for production deployment and support.
- Facilitate coordination of activities between the software development team and managed services provider.


System Architect

- Advisory role for knowledge transfer with previous efforts and legacy systems.
- Provide insight into legacy system and their architecture.
- Assist the project team in making informed decisions for technical design and system architecture.

Discovery Period - Sprint 0

Time Box, Roster and Goal	
Time Box	Discovery / Sprint 0 is expected to take this long to complete: Typically this period may last from 2-4 weeks, but could be longer depending on the project. The Discovery Period / Sprint 0 is over when the team can begin to build the product and the team has completed the Gate B - Authority to begin Sprinting evaluation.
Roster	These individuals and groups are expected to take part in Discovery / Sprint 0: - Core Scrum Team - Product Owner - Scrum Master - Team Members: Developers, Testers, Engineers, (whoever is building the product), etc. - Domain Subject Matter Experts - Information Systems Security Officer - Enterprise Architectural Engineers - End Users - Functional Subject Matter Experts - Anyone other stakeholder who will contribute to requirements gathering and preparing the Core Scrum Team to build
Goal	This is the goal of Discovery / Sprint 0: - To familiarize the team's understanding of the process and product to be developed. - To discover the product's requirements and establish the initial Product Backlog that will be continuously refined as the project progresses and product is incrementally developed and delivered.

ATF Agile Process Map

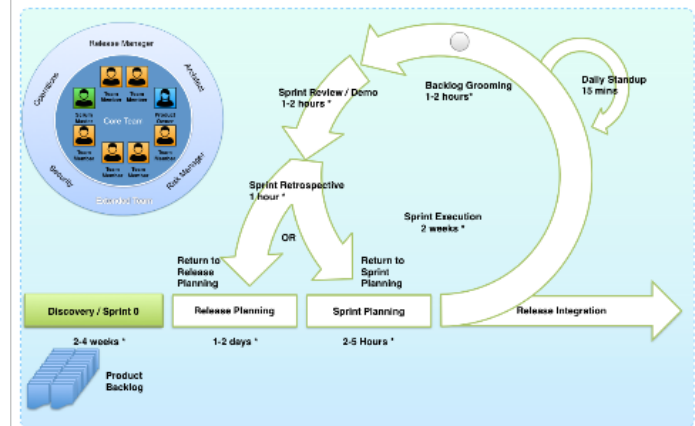

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook Sections

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

Release Planning

Sprint Planning

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Discovery / Sprint 0: • Identified Core Scrum Team (development team) • ATF Agile Training materials
Process	These activities are expected to take place during the Discovery / Sprint 0 session(s): • Kickoff Meeting for Scope and Admin items ◦ Attendees: Product Owner, Scrum Master, Stakeholders ◦ Outcome: Identification of Project Vision, desired skillsets, logistical items (seating, software, infrastructure) ◦ Benefit: Scope is clarified for all parties to ensure everyone is in the correct mindset and clear on the overall mission • Training Session(s) ◦ Attendees: Product Owner, Scrum Master, Team Members ◦ Outcome: Consistent understanding of the ATF Agile process and terminology. ◦ Benefits: Initial Agile/Scrum Training to level set team members to understand the process • Sticky Session(s) to identify User and High-Level functionality ◦ Attendees: Product Owner, Scrum Master, identified Team Members and Subject Mater Experts ◦ Outcome: Logical set of Users and high-level elements of functionality to be delivered during the execution of the project ◦ Benefit: Many team members contribute to creation of initial Product Backlog to cover proper breadth and depth, with these notes as a foundation for User Stories • Story Writing Session(s) ◦ Attendees: Product Owner, Scrum Master ◦ Outcome: Initial set of User Stories and Acceptance Criteria created by Product Owner and supported by Scrum Master ◦ Benefit: Product Owner references sticky note groups identified in previous session to create first User Stories • Review Session(s) ◦ Attendees: Product Owner, Scrum Master. Team Members ◦ Outcome: Team Members understand initial set of User Stories after discussing with Product Owner ◦ Benefit: Team gets to view the User Stories that were crafted from the sticky note groups that they created • Estimation Session(s) ◦ Attendees: Product Owner, Scrum Master. Team Members ◦ Outcome: Initial set of User Stories estimated at a Story-Level by Team Members ◦ Benefit: Team Members can compare items relative to each other more accurately since they contributed to the content • Order/Prioritization Session(s) ◦ Attendees: Product Owner, Scrum Master ◦ Outcome: Product Backlog that has User Stories that are ordered by priority ◦ Benefit: Product Owner can concentrate on ordering items that have the most business value as the first that the team will action • Risk/Dependency Session(s) ◦ Attendees: Product Owner, Scrum Master, Team Members ◦ Outcome: Listed User Story/Epic dependencies, risks and blockers/impediments to associated User Stories ◦ Benefit: Identifies impediments and blockers so they can be resolved prior to execution of the User Story/Epic Complete the required ATF Documentation to begin development (see Outputs list).

ATF Agile Playbook and Agile Tool Suite

Outputs	These items are expected as an output of the Discovery / Sprint 0:																																	
	<table> <tr> <th>Name</th><th>Description</th></tr> <tr> <td colspan="2">Responsibility : Information System Security Office (ISSO) (4)</td></tr> <tr> <td>FIPS 199 - Classification of the System</td><td>The FIPS 199 Categorization Worksheet is used to categorize the system by type, criticality, exposure, and data elements.</td></tr> <tr> <td>Privacy Threshold Analysis</td><td>The PTA is an administrative form created by the Privacy Office to efficiently and effectively identify the use of PII.</td></tr> <tr> <td>System Designation Memo</td><td></td></tr> <tr> <td>System Profile</td><td>Provides general, management, data, technical, security and privacy system profile information.</td></tr> <tr> <td colspan="2">Responsibility : ITCS (1)</td></tr> <tr> <td>508 Compliance Determination</td><td></td></tr> <tr> <td colspan="2">Responsibility : Scrum Team (8)</td></tr> <tr> <td>Agile Communications Plan</td><td>Establishes the recurring meetings and the names of the Core Team and Extended Team.</td></tr> <tr> <td>Architecture Diagram</td><td>Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.</td></tr> <tr> <td>Product Backlog of User Stories</td><td></td></tr> <tr> <td>Product Roadmap</td><td>Establishes the mid range (6 month to 12 month) plan for the product.</td></tr> <tr> <td>Product Vision</td><td>Establishes the goal of the system to convey to others.</td></tr> <tr> <td>Request for Change (RFC)</td><td>Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.</td></tr> <tr> <td>Risk and Impediments</td><td>List of items used to identify risks and impediments to the completion of building the product.</td></tr> <tr> <td>Test Strategy</td><td>Establishes the level of testing to be completed (expected to vary depending on the product).</td></tr> </table> Additionally, the development environment needs to be accessible by development team before their work can begin.	Name	Description	Responsibility : Information System Security Office (ISSO) (4)		FIPS 199 - Classification of the System	The FIPS 199 Categorization Worksheet is used to categorize the system by type, criticality, exposure, and data elements.	Privacy Threshold Analysis	The PTA is an administrative form created by the Privacy Office to efficiently and effectively identify the use of PII.	System Designation Memo		System Profile	Provides general, management, data, technical, security and privacy system profile information.	Responsibility : ITCS (1)		508 Compliance Determination		Responsibility : Scrum Team (8)		Agile Communications Plan	Establishes the recurring meetings and the names of the Core Team and Extended Team.	Architecture Diagram	Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.	Product Backlog of User Stories		Product Roadmap	Establishes the mid range (6 month to 12 month) plan for the product.	Product Vision	Establishes the goal of the system to convey to others.	Request for Change (RFC)	Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.	Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.	Test Strategy
Name	Description																																	
Responsibility : Information System Security Office (ISSO) (4)																																		
FIPS 199 - Classification of the System	The FIPS 199 Categorization Worksheet is used to categorize the system by type, criticality, exposure, and data elements.																																	
Privacy Threshold Analysis	The PTA is an administrative form created by the Privacy Office to efficiently and effectively identify the use of PII.																																	
System Designation Memo																																		
System Profile	Provides general, management, data, technical, security and privacy system profile information.																																	
Responsibility : ITCS (1)																																		
508 Compliance Determination																																		
Responsibility : Scrum Team (8)																																		
Agile Communications Plan	Establishes the recurring meetings and the names of the Core Team and Extended Team.																																	
Architecture Diagram	Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.																																	
Product Backlog of User Stories																																		
Product Roadmap	Establishes the mid range (6 month to 12 month) plan for the product.																																	
Product Vision	Establishes the goal of the system to convey to others.																																	
Request for Change (RFC)	Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.																																	
Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.																																	
Test Strategy	Establishes the level of testing to be completed (expected to vary depending on the product).																																	

Other Items

Work required by ATF in coordination with Discovery Period / Sprint 0:

Change Control Board	Activities driven by the CCB team will need support by the Scrum Team: - Submit your RFC on Friday by noon https://cit.atf.gov/vpn/index.html - Present your RFC to the CCB on the following Wednesday - Reviews and provides decision (approval/rejection) of RFCs
Operations	Activities driven by the Operations team may need support by the Scrum Team: RFC's request for the creation of the environments (which are scanned by Security before being released to the Scrum Team)


Next Steps: Release Planning

Release Planning

Time Box, Roster and Goal

Time Box	Release Planning is expected to take this long to complete: Varies based on the size and scope of the release, however generally they fall between 4 hours to 2 days.
Roster	These individuals and groups are expected to take part in Release Planning: - Core Scrum Team - Product Owner - Scrum Master - Team Members - Domain Subject Matter Experts (optional) - Information Systems Security Officer - Enterprise Architectural Engineers - End Users - Functional Subject Matter Experts - Anyone other stakeholder who will contribute to requirements gathering and preparing the Core Scrum Team to build
Goal	This is the goal of Release Planning: Identify the functionality that will be included within the context of a release.

ATF Agile Process Map

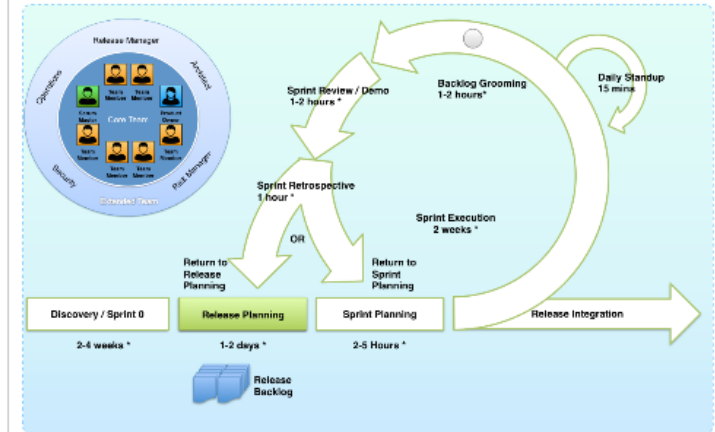

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook Sections

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

Sprint Planning

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Release Planning session(s): • Product Vision • Product Roadmap • Product Backlog (User Stories) ◦ Product Backlog contains enough User Stories to fill a release (set of Sprints) ◦ Stories have been relatively estimated by Team Members at Story-Point Level, not Task or Hour level ◦ Product Backlog has been ordered/prioritized by Product Owner with input from stakeholders and business owners ◦ Target Velocity has been determined based off of previous Sprint activity or best estimate if previous data is unavailable.																												
Process	These activities are expected to take place during the Release Planning session(s): • Meeting(s) to determine the <u>minimum viable product</u> for a release. • Review the <u>projected velocity</u> against the Release Backlog and estimate the delivery time of the product. • Plan out the schedule of activities post Sprints (see Release Integration and Release Deployment).																												
Outputs	These items are expected as an output of the Release Planning session(s): <table border="1"> <thead> <tr> <th>Name</th><th>Description</th></tr> </thead> <tbody> <tr> <td colspan="2">Responsibility : Information System Security Office (ISSO) (2)</td></tr> <tr> <td colspan="2">Security Implementation Statement</td></tr> <tr> <td colspan="2">System Security Plan</td></tr> <tr> <td colspan="2">Responsibility : Scrum Team (9)</td></tr> <tr> <td>Architecture Diagram</td><td>Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.</td></tr> <tr> <td>Failover Plan</td><td>Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions to recover the system should the implementation fail.</td></tr> <tr> <td>Implementation Plan</td><td>Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides a list of detailed instructions used to deploy a product.</td></tr> <tr> <td>OM Manual</td><td>Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides guidance to the Operations team on the regular maintenance required for the product to perform appropriately within an environment.</td></tr> <tr> <td>Release Backlog of User Stories</td><td>Establishes the planned list of User Stories to be completed during the course of a Release (multiple Sprints).</td></tr> <tr> <td>Release Burndown Chart</td><td>A chart that provides the total number of User Story points planned for the release and plots the burndown sprint over sprint within the release.</td></tr> <tr> <td>Release Schedule</td><td>Establishes the expected schedule of a Release, to include all planned Sprints and Post Sprint activities.</td></tr> <tr> <td>Training Plan</td><td>Planned for in Release Planning, completed prior to Release Integration (as necessary).</td></tr> <tr> <td>User Manual</td><td>Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions for use of the system.</td></tr> </tbody> </table>	Name	Description	Responsibility : Information System Security Office (ISSO) (2)		Security Implementation Statement		System Security Plan		Responsibility : Scrum Team (9)		Architecture Diagram	Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.	Failover Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions to recover the system should the implementation fail.	Implementation Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides a list of detailed instructions used to deploy a product.	OM Manual	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides guidance to the Operations team on the regular maintenance required for the product to perform appropriately within an environment.	Release Backlog of User Stories	Establishes the planned list of User Stories to be completed during the course of a Release (multiple Sprints).	Release Burndown Chart	A chart that provides the total number of User Story points planned for the release and plots the burndown sprint over sprint within the release.	Release Schedule	Establishes the expected schedule of a Release, to include all planned Sprints and Post Sprint activities.	Training Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary).	User Manual	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions for use of the system.
Name	Description																												
Responsibility : Information System Security Office (ISSO) (2)																													
Security Implementation Statement																													
System Security Plan																													
Responsibility : Scrum Team (9)																													
Architecture Diagram	Establishes the architectural design of the system to be built to use as reference. After this document is created, it is periodically reviewed and updated.																												
Failover Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions to recover the system should the implementation fail.																												
Implementation Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides a list of detailed instructions used to deploy a product.																												
OM Manual	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides guidance to the Operations team on the regular maintenance required for the product to perform appropriately within an environment.																												
Release Backlog of User Stories	Establishes the planned list of User Stories to be completed during the course of a Release (multiple Sprints).																												
Release Burndown Chart	A chart that provides the total number of User Story points planned for the release and plots the burndown sprint over sprint within the release.																												
Release Schedule	Establishes the expected schedule of a Release, to include all planned Sprints and Post Sprint activities.																												
Training Plan	Planned for in Release Planning, completed prior to Release Integration (as necessary).																												
User Manual	Planned for in Release Planning, completed prior to Release Integration (as necessary). Provides instructions for use of the system.																												

Other Items

Work required by ATF in coordination with Release Planning that may materialize as new User Stories or tasks of User Stories to account for related work inside a Sprint inside the Release.

	none
--	------


Next Steps: Sprint Planning

Sprint Planning

Time Box, Roster and Goal

Time Box	Sprint Planning is expected to take this long to complete: - Typically 2 to 5 hours depending on the length of the Sprint and the team's familiarity of the User Stories being included in the Sprint Backlog. - Rule of thumb is <2 hours for each week of Sprint. E.g. 2 week Sprint < 4 hours planning.
Roster	These individuals and groups are expected to take part in Sprint Planning: - Core Scrum Team - Product Owner - Scrum Master - Team Members - Subject Matter Experts (as necessary / optional)
Goal	This is the goal of Sprint Planning: - Team discusses Product Backlog items with Product Owner to confirm consistent understanding - Team finalizes the items to accomplish in the upcoming Sprint (the Sprint Backlog), based on the priority/order given by the Product Owner within the limits of the Team's capacity - Team creates a sufficiently detailed plan to accomplish items in the Sprint Backlog

ATF Agile Process Map

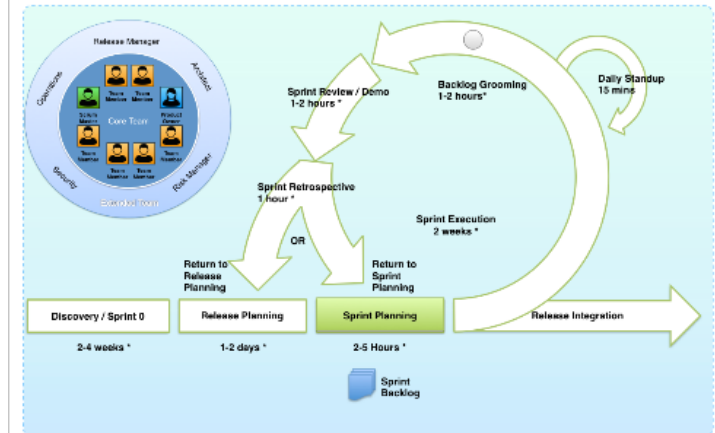

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

[Sprint Planning](#)

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Sprint Planning session: • Release Backlog • Product Backlog (User Stories) • Team availability for the days in the new Sprint
Process	These activities are expected to take place during the Release Planning session(s): • Confirm Prioritization ▫ Attendees: Product Owner, Scrum Master, Team Members ▫ Outcome: Selected Sprint Backlog based on priorities set by the Product Owner ▫ Benefit: Team knows what the Product Owner wants to focus on for the Sprint ▫ Best Practice: Team identifies a realistic number of hours individuals can be productive building the product. Even with 8 hours of work per day, individuals are distracted by non-Sprint related meetings, emails, discussions, water breaks, etc. Individuals also need to account for hours they would not be working on product (e.g. Sprint Planning, Sprint Retrospective, Sprint Review, Backlog Grooming sessions) that are crucial to success, but take away from availability • Capacity Planning ▫ Attendees: Scrum Master, Team Members ▫ Outcome: Team capacity for the Sprint ▫ Benefit: Team knows how many hours each individual can commit to during the Sprint ▫ Best Practice: Team identifies a realistic number of hours individuals can be productive building the product. Even with 8 hours of work per day, individuals are distracted by non-Sprint related meetings, emails, discussions, water breaks, etc. Individuals also need to account for hours they would not be working on product (e.g. Sprint Planning, Sprint Retrospective, Sprint Review, Backlog Grooming sessions) that are crucial to success, but take away from availability to build product. Rule of thumb is 6 hours per full day within the Sprint, but the team will norm on its own calculation. • Tasking and Ownership ▫ Attendees: Product Owner, Scrum Master, Team Members ▫ Outcome: Team tasks and assignments ▫ Benefit: Team knows what tasks (technical and non-technical) are necessary to completed the Sprint Backlog ▫ Best Practice: Team collectively identifies each of the tasks necessary to complete a single User Story. Then individuals within the Team signup or volunteer to take responsibility for the individual tasks and identify how much time it will take them to accomplish the task. Sometimes it good to think of it as "how much time do you want to set aside to get this accomplished?" After the team agrees all the tasks have been identified and associated with an individual within the team, move onto the next User Story in the Sprint Backlog. Repeat until the team has no more capacity to take on additional work for the Sprint. ▫ Best Practice: Continuously monitor the amount of time individuals are committing themselves. Work needs to be distributed through the entire team. ▫ Best Practice: Allow individuals to identify their own hour commitments. Some tasks may be quick for some team members, but longer for others. This is a reality within a team and individuals should not be discouraged from speaking freely about their individual time estimates or the team will run the risk of over/under estimating tasks to avoid shame. ▫ Best Practice: Individuals should not sign up for more than their capacity will allow to avoid burnout. It's important to maintain a consistent and sustainable pace. ▫ Best Practice: Even though the meeting may seem like a waste of time, the Product Owner needs to be in the meeting to answer questions that may arise during the discussion of tasks for User Stories. Often, the identification of tasks elevates differences of opinion of what is to be developed/built/accomplished. The Product Owner is then able to clarify the details, which will ensure the proper execution plan (tasks) is identified for each User Story. The Team should never have to say "we need to follow up with the Product Owner later."

ATF Agile Playbook and Agile Tool Suite

Outputs	These items are expected as an output of the Sprint Planning:	
	Name	Description
	☐ Responsibility : Scrum Team (2)	
	Sprint Backlog (User Stories)	List of User Stories that the team has committed to during a Sprint.
	Sprint Plan (User Stories and Tasks)	User Stories along with their associated tasks to be executed during a Sprint.

Other Items	
	none

Next Steps: Sprint Execution


Immediately begin work and update the status of User Stories and Tasks to "In Progress" as appropriate.

Sprint Execution

Time Box, Roster and Goal

Time Box	Sprints are expected to take this long to complete: 1-4 weeks, depending on the cadency chosen by the team and documented in the ATF Agile Communication Plan. - its is important to maintain a consistent Sprint period throughout a Release to be able to reliably use the team's Velocity to use in schedule forecasting.
Roster	These individuals and groups are expected to take part in Sprints: - Core Scrum Team - Product Owner - Scrum Master - Team Members
Goal	This is the goal of Sprints: Develop working product.

ATF Agile Process Map

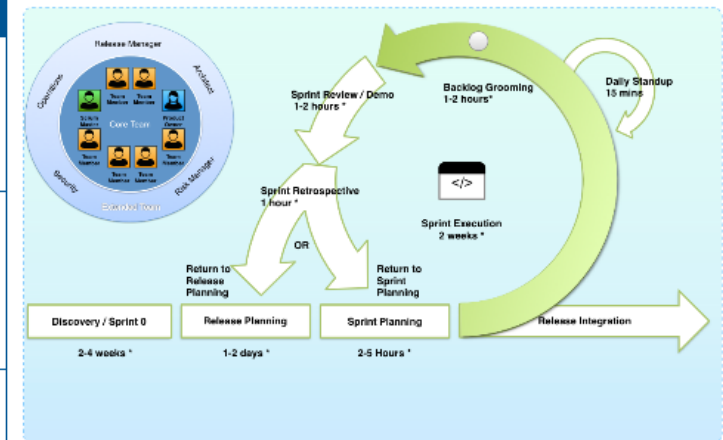

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

[Sprint Planning](#)

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Sprint: • Sprint Backlog • Team
--------	---

Process	These activities are expected to take place during the Sprint: • Daily Development and Testing Activities ◦ Varies based on the product/project, but ultimately the process will develop working product. ◦ E.g. Software Development ▪ Write code ▪ Unit Test code ▪ Integration Test code ▪ Quality Test code ▪ Functional Test code ▪ Regression Test code ▪ User Acceptance Test code (performed by the Product Owner) • Daily Stand-up (aka Daily Scrum) ◦ Alignment of the team members on the recent accomplishments, current tasks and current impediments • Backlog Grooming Session(s) ◦ Preparation for the upcoming Sprint, the team meets to refine the User Stories for the upcoming Sprints in greater detail. • Best Practice: Continuous Integration with Automated Unit Testing, Automated Regression Testing,, Automated Performance Testing, Automated Integration Testing Automated Quality Testing and Automated Vulnerability Testing
---------	--

Outputs	These items are expected as an output of the Sprint: <table> <thead> <tr> <th>Name</th><th>Description</th></tr> </thead> <tbody> <tr> <td colspan="2">Responsibility : Scrum Team (4)</td></tr> <tr> <td>Risk and Impediments</td><td>List of items used to identify risks and impediments to the completion of building the product.</td></tr> <tr> <td>Sprint Burndown Chart</td><td></td></tr> <tr> <td>Test Cases</td><td>Defines the Test Cases & Steps that will be used to validate the functionality being developed works as requested</td></tr> <tr> <td>Working Product</td><td>The developed, tested and potentially deliverable product.</td></tr> </tbody> </table>	Name	Description	Responsibility : Scrum Team (4)		Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.	Sprint Burndown Chart		Test Cases	Defines the Test Cases & Steps that will be used to validate the functionality being developed works as requested	Working Product	The developed, tested and potentially deliverable product.
Name	Description												
Responsibility : Scrum Team (4)													
Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.												
Sprint Burndown Chart													
Test Cases	Defines the Test Cases & Steps that will be used to validate the functionality being developed works as requested												
Working Product	The developed, tested and potentially deliverable product.												

Other Items


	None
--	------

Next Steps: Sprint Review (aka Sprint Demo)

Daily Stand-up

Time Box, Roster and Goal	
Time Box	Daily Stand-up is expected to take this long to complete: - once per day 10-15 mins.
Roster	These individuals and groups are expected to take part in the Daily Stand-up: - Scrum Master - Team Members - Product Owner (optional)
Goal	This is the goal of Daily Stand-up: - Impediments are identified for later action, outside of this particular session - Alignment of activities between team members, especially those with extra capacity - Offline meetings are identified during discussion centric to current sprint activities

ATF Agile Process Map

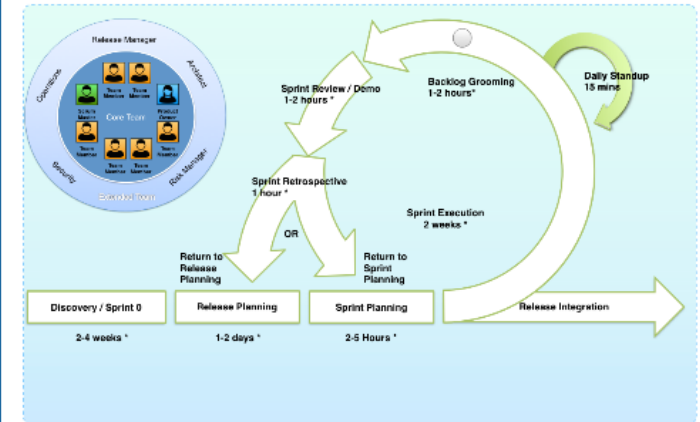

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

[Sprint Planning](#)

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Daily Stand-up: • Sprint Story Board and Task Board and impediments								
Process	These activities are expected to take place during the Daily Stand-up: • Standup ◦ Attendees: Scrum Master, Team Members, Product Owner (optional) ◦ Outcome: Updated Team and identified impediments ◦ Benefit: Team is aware and aligned (as appropriate) with each other's activities ◦ Best Practice: Ensure items maintain focus on the User Stories and don't veer off to unrelated items (e.g. recent family vacation, sports teams or tabloid excerpts) ◦ Best Practice: While its important to retain focus on the tasks and user stories, its also important to maintain team morale, so sometimes let the vacation and sport stories go on, but make sure to corral the group back after 30 seconds or so. Use good judgment and don't always be too strict. ◦ Best Practice: Ensure focus remains on current sprints activities, not past or future.								
Outputs	Updates to these items is expected as an output of the Daily Stand-up: <table> <thead> <tr> <th>Name</th><th>Description</th></tr> </thead> <tbody> <tr> <td colspan="2">Responsibility : Scrum Team (2)</td></tr> <tr> <td>Risk and Impediments</td><td>List of items used to identify risks and impediments to the completion of building the product.</td></tr> <tr> <td>Sprint Plan (User Stories and Tasks)</td><td>User Stories along with their associated tasks to be executed during a Sprint.</td></tr> </tbody> </table>	Name	Description	Responsibility : Scrum Team (2)		Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.	Sprint Plan (User Stories and Tasks)	User Stories along with their associated tasks to be executed during a Sprint.
Name	Description								
Responsibility : Scrum Team (2)									
Risk and Impediments	List of items used to identify risks and impediments to the completion of building the product.								
Sprint Plan (User Stories and Tasks)	User Stories along with their associated tasks to be executed during a Sprint.								

Other Items

	None
--	------


Next Steps: Continue with the Sprint Execution

Backlog Grooming

Time Box, Roster and Goal

Time Box	Backlog Grooming is expected to take this long to complete: 1-2 hours
Roster	These individuals and groups are expected to take part in Backlog Grooming: - Core Scrum Team - Product Owner - Scrum Master - Team Members: Developers, Testers, Engineers, (whoever is building the product), etc. - Domain Subject Matter Experts (optional) - Information Systems Security Officer - Enterprise Architectural Engineers - End Users - Functional Subject Matter Experts - Anyone other stakeholder who will contribute to requirements gathering and preparing the Core Scrum Team to build
Goal	This is the goal of Backlog Grooming: - Generate updated Product Backlog where higher priority stories have been discussed first "Groomed" or "refined" User Stories where descriptions and acceptance criteria are understood by all - Generate estimates for new items and (sometimes) update to previous Relative Complexity Estimates

ATF Agile Process Map

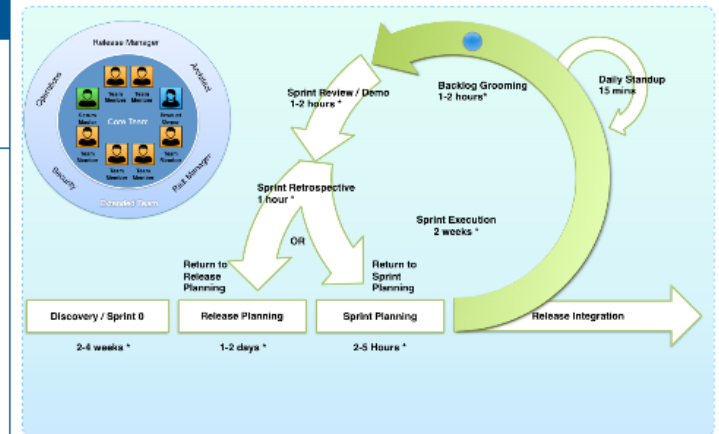

* Actual duration of activity is unique to the given project's scope, schedule and team

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

[Sprint Planning](#)

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Backlog Grooming: • Product Backlog • Release Backlog • Expected next Sprint Backlog (if already identified)
Process	These activities are expected to take place during the Sprint: • Backlog Grooming Session ◦ Primary focus is preparing User Stories for the next Sprint. ◦ After the immediate next Sprint's Backlog is refined, move on to the next set of stories beyond that immediate next Sprint. ◦ Best Practices: Make sure to ask all pertinent questions in the Backlog Grooming. You shouldn't go into Sprint Planning with a list of questions. ◦ Best Practice: Planning Poker
Outputs	These items are expected as an output of the Sprint: ◦ Fully defined and understood and properly Sized User Story sized User Stories with their Relative Complexity Estimates for the next Sprint.

Other Items

	None
--	------


Next Steps: Sprint Execution

The team should return to development / building product.

Sprint Review

Time Box, Roster and Goal	
Time Box	The Sprint Review is expected to take this long to complete: 2 to 4 hours (target one hour for each week of Sprint)
Roster	These individuals and groups are expected to take part in the Sprint Review: - Core Scrum Team - Product Owner - Scrum Master - Developers, Testers, Engineers, (whoever is building the product), etc. - Domain Subject Matter Experts (optional) - Information Systems Security Officer - Enterprise Architectural Engineers - End Users - Functional Subject Matter Experts
Goal	These are the goals of the Sprint Review: - Accomplishments are reviewed and demonstrated to participants - Feedback is gathered to be incorporated into team activities - Potential re-prioritization of Product Backlog items following discussions

ATF Agile Process Map

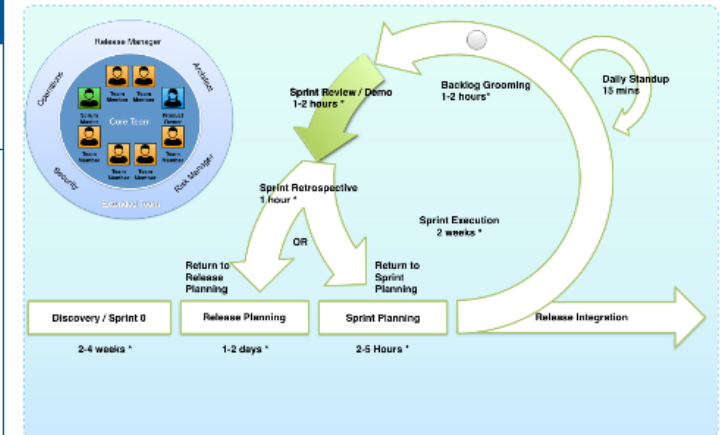

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

Roles and Responsibilities

Discovery Period - Sprint 0

Gate B - Authority to begin Sprinting

Release Planning

Sprint Planning

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Sprint Review: • Release Burndown • Sprint Backlog • Working product
Process	These activities are expected to take place during the Sprint: • Sprint Review / Demonstration ◦ Review of all the completed User Stories: ▪ Reading of a single User Story ▪ Demonstration of the User Story's functionality that was build during the Sprint ▪ Solicit feedback from the participants in the Sprint Review ▪ Repeat for all completed User Stories ◦ Review of the Incomplete User Stories that are still in progress: ▪ Reading of a single User Story ▪ Briefly discuss why it was not complete ▪ Repeat for remaining incomplete User Stories ◦ Review of any blocked User Stories and why they were blocked from being completed ▪ Reading of a single User Story ▪ Briefly discuss the blocker and solicit help from individuals/groups attending the Sprint Review if they are in a position to help remove a blocker ▪ Repeat for all blocked User Stories ◦ Best Practice: Include a review of the User Stories currently slated for the next Sprint. The feedback from the audience may be useful and it will give others a heads up if you intend to lean on their support to complete specific User Stories. ◦ Best Practice: For teams that are integrated with other team's efforts, holding the Sprint Review together with multiple teams will help align efforts as necessary. ◦ Best Practice: Review of the Release Burndown during the Sprint Review helps to provide context and remaining work to be done in the release to the group. ◦ Best Practice: In the opening of your Sprint Review, its good to briefly introduce the purpose of the project and/or release as well as the structure and purpose of the Sprint Review. It helps to ensure everyone is on the same page regarding the scope of work as well as inform those who may not have attended a Sprint Review in the past.
Outputs	These items are expected as an output of the Sprint Review: • Feedback that may lead to refinement of future User Stories.

Other Items


	None
--	------

Next Steps: Sprint Retrospective

Sprint Retrospective

Time Box, Roster and Goal	
Time Box	Sprint Retrospectives are expected to take this long to complete: Approximately 1 hour
Roster	These individuals and groups are expected to take part in Sprint Retrospectives: - Scrum Master - Team Members - Product Owner (optional)
Goal	This is the goal of Sprint Retrospectives: - Previous Sprint is reviewed by Team members - Items that went well and items that need improvement are identified - Plan is created to address items in upcoming Sprint

ATF Agile Process Map

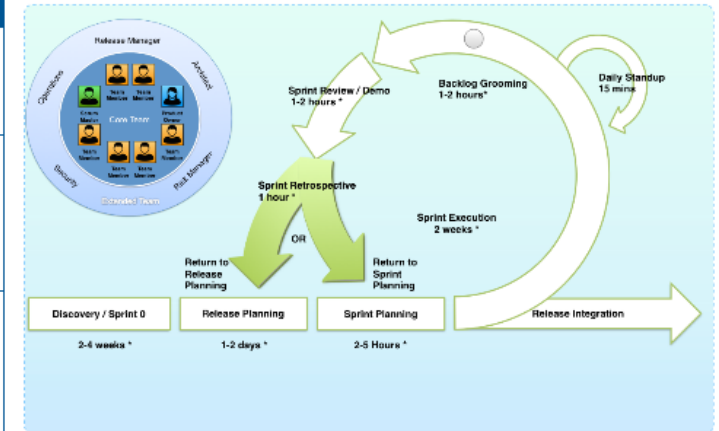

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

[Roles and Responsibilities](#)

[Discovery Period - Sprint 0](#)

Gate B - Authority to begin Sprinting

[Release Planning](#)

[Sprint Planning](#)

Sprint Execution

Daily Stand-up

Backlog Grooming

[Sprint Review](#)

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs	These inputs are expected to be available in order to begin the Sprint Retrospective: - Team experiences from Sprint - Previous Sprint Retrospective data						
Process	These activities are expected to take place during the Sprint Retrospective: - Retrospective - Identify the positive, negative and action plan to provide a improved process Best Practice: Sail Boat Method - Associate the positive with the wind behind the sail that pushes a Sail Boat (the project) forward - Associated negative things with an Anchor that hold the Sail Boat (the project) back - Identify the action plan to improve Best Practice: Star Method - Sticky pads are distributed to each team member - Team members write comments on the sticky pads, one comment per sticky and aligned with 1 of in 5 different categories (Do More, Keep Doing, Do Less, Stop Doing, Start Doing) - Review each sticky in their appropriate section of the "Star" as a group and identify action items from each as appropriate Best Practice: Review previous Retrospectives to ensure you're adhering to those previously identified best practices						
Outputs	These items are expected as an output of the Sprint Retrospective: <table> <thead> <tr> <th>Name</th><th>Description</th></tr> </thead> <tbody> <tr> <td colspan="2">Responsibility : (1)</td></tr> <tr> <td>Sprint Retrospective Action Plan</td><td>The Sprint Retrospective is an opportunity for the Scrum Team to inspect itself and create a plan for improvements to be enacted during the next Sprint.</td></tr> </tbody> </table>	Name	Description	Responsibility : (1)		Sprint Retrospective Action Plan	The Sprint Retrospective is an opportunity for the Scrum Team to inspect itself and create a plan for improvements to be enacted during the next Sprint.
Name	Description						
Responsibility : (1)							
Sprint Retrospective Action Plan	The Sprint Retrospective is an opportunity for the Scrum Team to inspect itself and create a plan for improvements to be enacted during the next Sprint.						

Other Items

	None
--	------

Next Steps: Sprint Planning or Release Planning and Release Integration


- After completing the Sprint Retrospective the team should begin the [Sprint Planning](#) for the next Sprint
- If this was the last Sprint in the Release, then the team product should move to [Release Integration](#) and the team should begin [Release Planning](#)

Release Integration

The Core Scrum Team is not the primary working group within this portion of the project life cycle. Release Integration is performed by supporting teams responsible for verifying the product's functionality, performance and security. The Core Scrum Team will need to address any discovered vulnerabilities or defects based on the prioritization of the Product Owner.

Time Box, Roster and Goal	
Time Box	Release Integration is expected to take this long to complete: Varies depending on the size and scope of the release
Roster	These individuals and groups are expected to take part in Release Integration: - Independent Verification & Validation (IV&V) Team - Information System Security Officer (ISSO) - OST Project Lead - Operations Team - Core Scrum Team
Goal	This is the goal of Release Integration: - Certify a Release meets security and functional requirements by groups outside the Core Scrum Team - Operations team can execute the deployment and roll back as necessary

ATF Agile Process Map

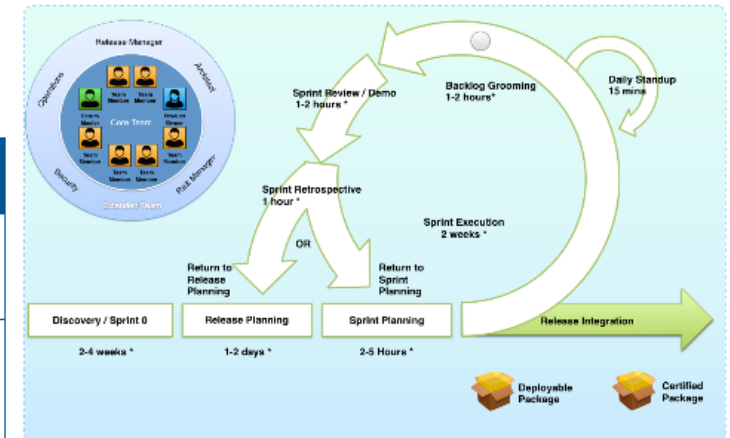

* Actual duration of activity is unique to the given project's scope, schedule and team.

Agile Playbook

Name

Introduction to the Agile Playbook

Gate A - Authority to Initiate a Project

Roles and Responsibilities

Discovery Period - Sprint 0

Gate B - Authority to begin Sprinting

Release Planning

Sprint Planning

Sprint Execution

Daily Stand-up

Backlog Grooming

Sprint Review

Sprint Retrospective

Release Integration

Gate C - Authority to move to Production

Inputs, Processes and Outputs

Inputs

These inputs are expected to be available in order to begin the Release Integration:

- Implementation Plan (as necessary)
- OM Manual (as necessary)
- Training Plan (as necessary)
- User Manual (as necessary)
- Release Backlog
- Architecture Diagram
- Failover Plan
- System Security Plan

Process

These activities are expected to take place during the Release Integration:

- Deploy release to TEST environment
 - Submit Work Request to Operations Team and reference the approved RFC
 - Operations Team deploys to the TEST environment following instructions outlined in the Implementation Plan
- IVV Testing (subject to the [Test Strategy](#))
 - Execute tests
 - Report any defects to the appropriate parties and perform confirmation of fixes
- Security Testing
 - Certification and Accreditation (C&A) process
 - Execute Vulnerability Tests (Hailstorm, Nessus, AppDetective, etc.)
 - Report any vulnerabilities / defects to the appropriate parties and perform confirmation of fixes
- Fixing bugs discovered during Release Integration
 - Confirmed defects and bugs are documented as User Stories within the Product Backlog to be prioritized appropriately by the Product Owner
 - Scrum Team executes the "bug" User Stories within their Sprints that has already moved onto the next Release Backlog and deploys fix to the Release Integration
- [Gate C - Authority to Move to Production](#)
- **Example Scenario**
 - Release 1 has been released to TEST environment
 - Scrum Team is Sprinting and working on Release 2
 - Bug from Release 1 is introduced into the Release 2 backlog
 - Team addresses bug in Sprint 8 of Release 2 (this could potentially affect the Release 2 schedule)
 - Bug fix is completed in Sprint 8 and new Dimensions Baseline is created for Release 1 for Operations to deploy in the TEST environment for revalidation by the party that discovered the issue
 - Team continues working on Release 2 Backlog and addresses any future Release 1 bugs in their Sprint cycle as appropriate

ATF Agile Playbook and Agile Tool Suite

Outputs	These items are expected as an output of the Release Integration: <table border="1"> <thead> <tr> <th>Name</th><th>Description</th></tr> </thead> <tbody> <tr> <td colspan="2">☑ Responsibility : Govt Project Manager (2)</td></tr> <tr> <td>Interconnection Security Agreement (ISA)</td><td>Defines the data required by ATF, the communication path, data handling, protection requirements and procedures for the effective sharing of sensitive data and related information.</td></tr> <tr> <td>Memorandum of Understanding or Agreement (MOU-MOA)</td><td>Establishes an agreement between agencies regarding the development, management, operation and security of integrated inter/intra agency systems.</td></tr> <tr> <td colspan="2">☑ Responsibility : Information System Security Office (ISSO) (2)</td></tr> <tr> <td>Authority to Operate (ATO)</td><td></td></tr> <tr> <td>Contingency Plan</td><td>Provides IT recovery information and procedures to recover the a system following a disruption</td></tr> <tr> <td colspan="2">☑ Responsibility : Scrum Team (1)</td></tr> <tr> <td>Request for Change (RFC)</td><td>Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.</td></tr> </tbody> </table>	Name	Description	☑ Responsibility : Govt Project Manager (2)		Interconnection Security Agreement (ISA)	Defines the data required by ATF, the communication path, data handling, protection requirements and procedures for the effective sharing of sensitive data and related information.	Memorandum of Understanding or Agreement (MOU-MOA)	Establishes an agreement between agencies regarding the development, management, operation and security of integrated inter/intra agency systems.	☑ Responsibility : Information System Security Office (ISSO) (2)		Authority to Operate (ATO)		Contingency Plan	Provides IT recovery information and procedures to recover the a system following a disruption	☑ Responsibility : Scrum Team (1)		Request for Change (RFC)	Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.
Name	Description																		
☑ Responsibility : Govt Project Manager (2)																			
Interconnection Security Agreement (ISA)	Defines the data required by ATF, the communication path, data handling, protection requirements and procedures for the effective sharing of sensitive data and related information.																		
Memorandum of Understanding or Agreement (MOU-MOA)	Establishes an agreement between agencies regarding the development, management, operation and security of integrated inter/intra agency systems.																		
☑ Responsibility : Information System Security Office (ISSO) (2)																			
Authority to Operate (ATO)																			
Contingency Plan	Provides IT recovery information and procedures to recover the a system following a disruption																		
☑ Responsibility : Scrum Team (1)																			
Request for Change (RFC)	Provides approval for the environments to be created to support the effort and authorizes the work effort. It is created as necessary and reviewed by the Change Control Board as necessary.																		

Other Items

Work required by ATF in coordination with Release Integration:


Change Control Board	Reviews and provides decision (approval/rejection) of RFC to move the release to Production
----------------------	---

ATF Agile Tool Suite

Purpose

Goal: To provide the software and infrastructure necessary to support the ATF Agile Enablement effort. Ultimately, the goal is to improve the quality of software and reduce the time to deliver by replacing the traditional practice of applying quality control after development has completed.


History: The CI tools were initially stood up in an AWS cloud environment to demonstrate their effectiveness and prototype the integration. Subsequently, it has been deployed to the ATF Data Center and is now available for developer use.

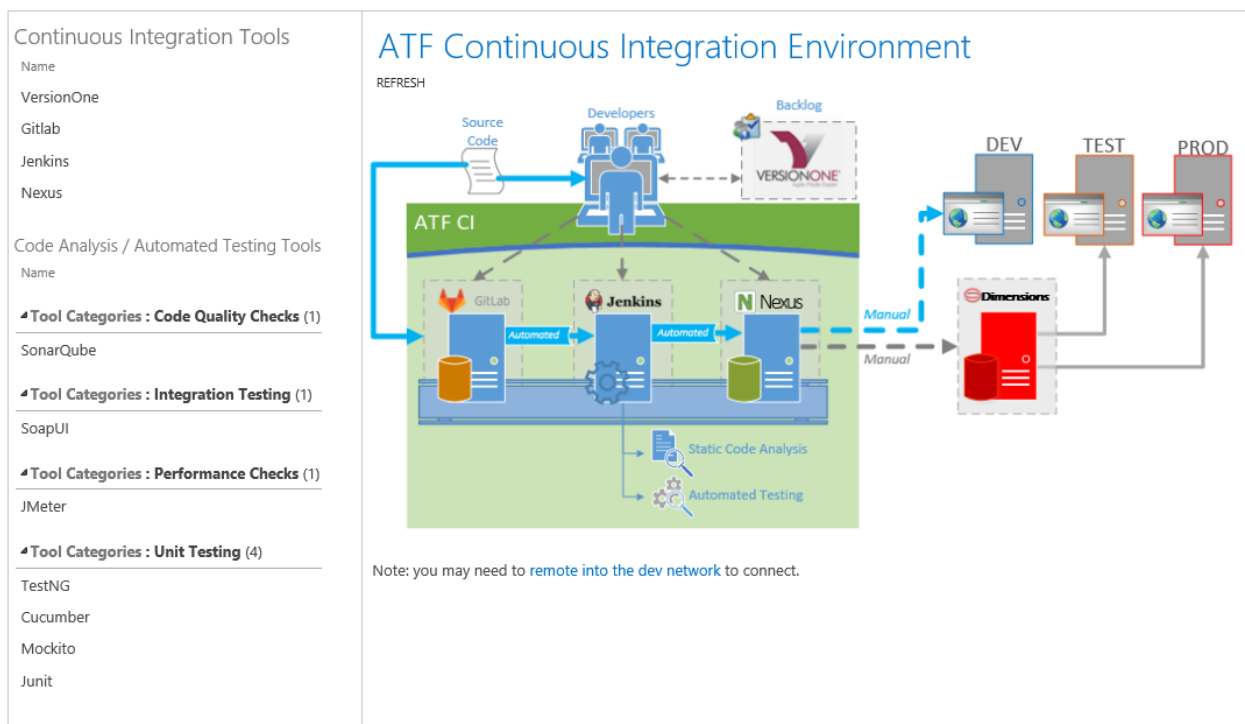

CI Maturity Spectrum

If you are just starting out, it's best to introduce automation slowly to ensure you don't take on too much and introduce too much change too quickly.

ATF Agile Playbook and Agile Tool Suite

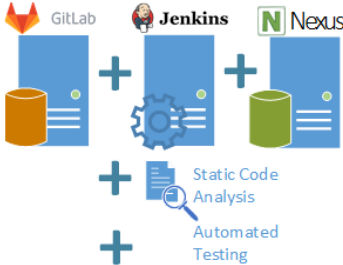Phase 1	Phase 2	Phase 3
Get your source code into the Gitlab repository. Storing your source code and committing changes on a daily basis will ensure your daily work is backed-up appropriately. Get started by with ATF's Gitlab.	Introduce automate builds using Jenkins. If your source code is something that can be compiled, use Jenkins to compile it on a regular basis, either at each Git commit or on a regularly schedule basis (daily or nightly). After you get started with Gitlab, move on to scheduling your Jenkins builds and have your binary's stored in Nexus.	Introduce automated tests in your Jenkins builds using the integrated tools available in the ATF CI environment. If your project needs a tool that's not listed, contact ci-support@atf.gov. When you're ready, incorporate Static Code Analysis and Automated Testing tools in your Jenkins jobs.
		

ATF's Automation Goals

ATF is slowly introducing these concepts of automation to ensure all necessary things are taking into account. As Continuous Integration is introduced, the ultimate goal will be to reach Continuous Delivery so that project teams can create and automate as much as possible, while maintaining the necessary manual controls required by ATF's environment.

Additionally, ATF leadership is reviewing options to improve the automated deployment strategy to address the manual processes to deploy to the DEV, TEST and PROD environments (illustrated in the ATF Continuous Integration Environment graphic above).
